



Brown & Root
INDUSTRIAL SERVICES, LLC.

WEEKLY CONSTRUCTION PROGRESS REPORT

Construct Field Houses, S. Atlanta and Carver High Schools

May 13, 2021

Prepared For: Atlanta Public Schools

Prepared By: Michael Bower



Figure 1 S. Atl – Flowwell Installation

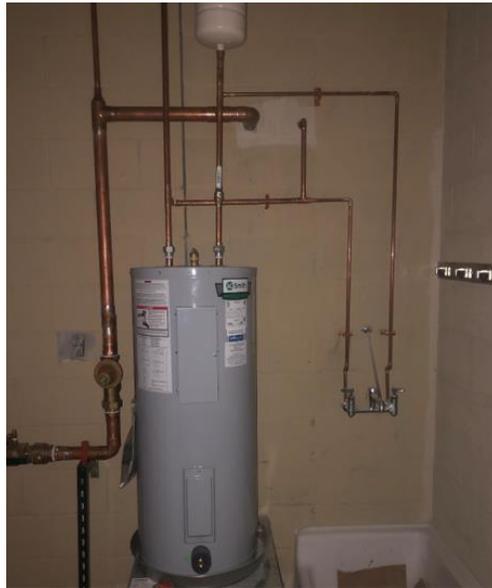


Figure 2 S. Atl – Plumbing Rough and Accessories



Figure 3 Carver – Block fill and first coat



Figure 4 Carver – Soffit



WEEKLY CONSTRUCTION PROGRESS REPORT

Construct Field Houses, S. Atlanta and Carver High Schools

May 13, 2021

Last Week's Activities:

- Carver HS – Exterior soffit electrical rough-in, steel field fix
- S. Atlanta HS – Brick pressure wash, mechanical and electrical rough, plumbing rough, install Flowell, block fill and first coat of paint.

This Week's Activities:

- Carver HS – block fill and first coat of paint, soffit and fascia materials delivered and installation started, plumbing material delivery.
- S. Atlanta HS – Flowell installation, fans installation, finish electrical rough above ceiling and ceiling closure inspection, misc. accessories.

Next Week's Activities:

- Carver HS – Plumbing rough-in, brick pressure wash, cmu tooth in to deck, MEP rough-in, interior doors.
- S. Atlanta HS – Mechanical inspection, complete sidewalk, toilet partitions.

Schedule:

- Revised Target Completion dates of 6/14 and 7/2 (S. Atl and Carver respectively) shows a slight expected improvement in the scheduled dated 3/5/21. The GC has shown improved manpower and progress consistently above and beyond previous efforts with Brown and Root continuing assistance with cash flow for the GC.

Budget:

- Construction Budget:
 - Carver: \$806,230
 - S. Atlanta: \$604,946
- Budget Status: On Budget
- Gross Billed to Date:
 - Carver: \$554,192
 - S. Atlanta: \$443,337
