



Weekly Construction Progress Report

Midtown High School

Week Ending: 4/23/2021

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP overhead and trim out in new addition building.
- Continue fire sprinkler on 4th floor of new addition.
- Continue Metal Panel Installation at New Addition.
- Painting in Performance Gym.
- Continue Patio Roofing system.
- Continue hardscapes on the East and Southeast Elevations.
- Continue Epoxy flooring in New Addition Restrooms.
- Continue VCT and flooring finishes in New Addition Building.
- Continue Terrazzo Installation on Second Floor of New Addition Building.
- Continue Multipurpose and CTAE build back in 8th street building.
- Dropping ceiling tiles in New Addition Building.

NEXT WEEK – 4.26.2021 – 4.30.2021

- Continue MEP overhead and trim out on Third, and Fourth floors of the new addition.
- Installing lights and Low-Voltage fixtures.
- Continue hardscapes on the East and South East Elevations. Begin prep for North Elevations.
- Continue Patio Roofing system.
- Continue Ceramic Tile Installation in Restrooms.
- Continue Metal Panel Installation.
- Continue Epoxy flooring in New Addition Restrooms.
- Continue Terrazzo Installation on Second Floor of New Addition Building.
- Continue VCT and Flooring Finishes in new Addition Building.
- Begin Curtainwall Installation at New Addition and C. Allen Building Bridge.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 27,826,691.43

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG
 - Tyler Cobb, PCG
 - Paul Cobb, PCG



Photo Updates

New Addition Classroom Progress




New Addition Classroom Progress



Photo Updates

Terrazzo Progress 2nd Floor of New Addition

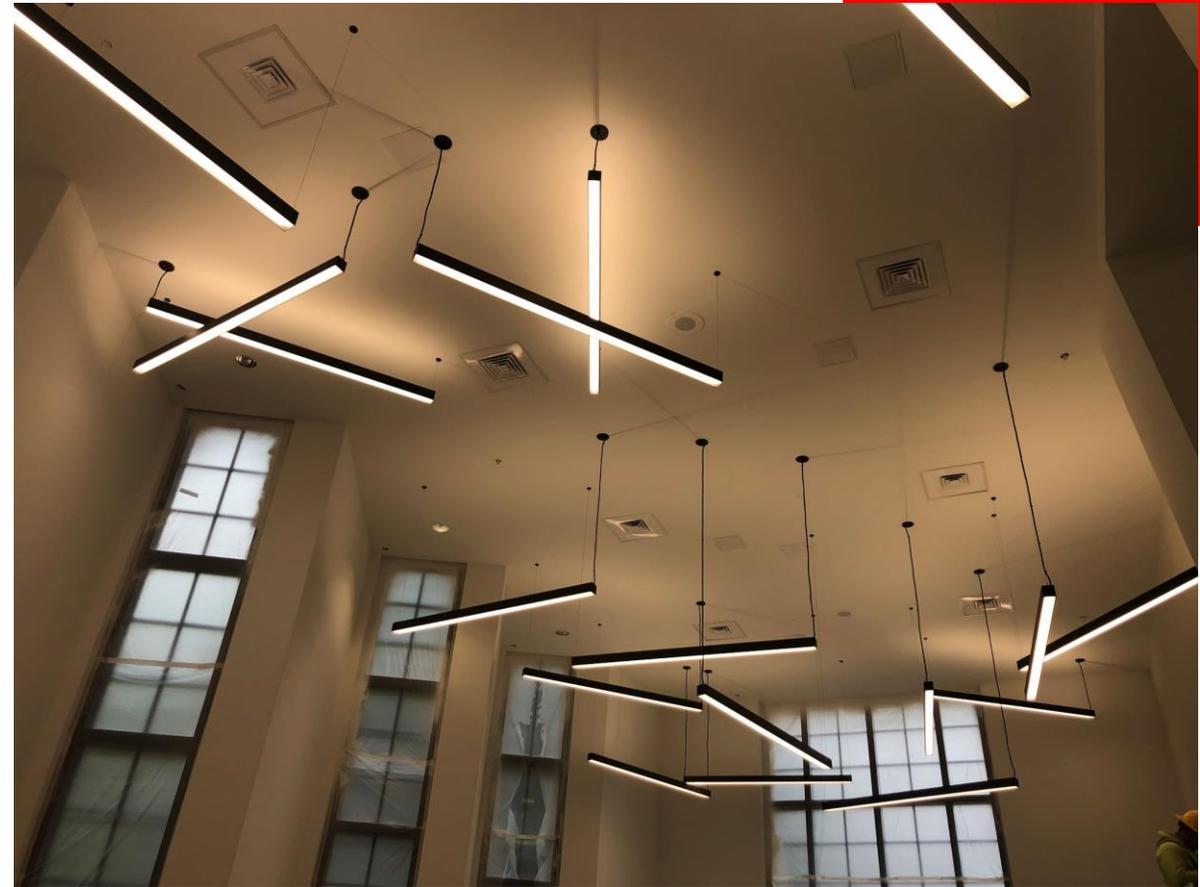


Light Fixtures Installed in New Addition
Media Center



Photo Updates

Marker and Tack Boards Installed in
New Addition

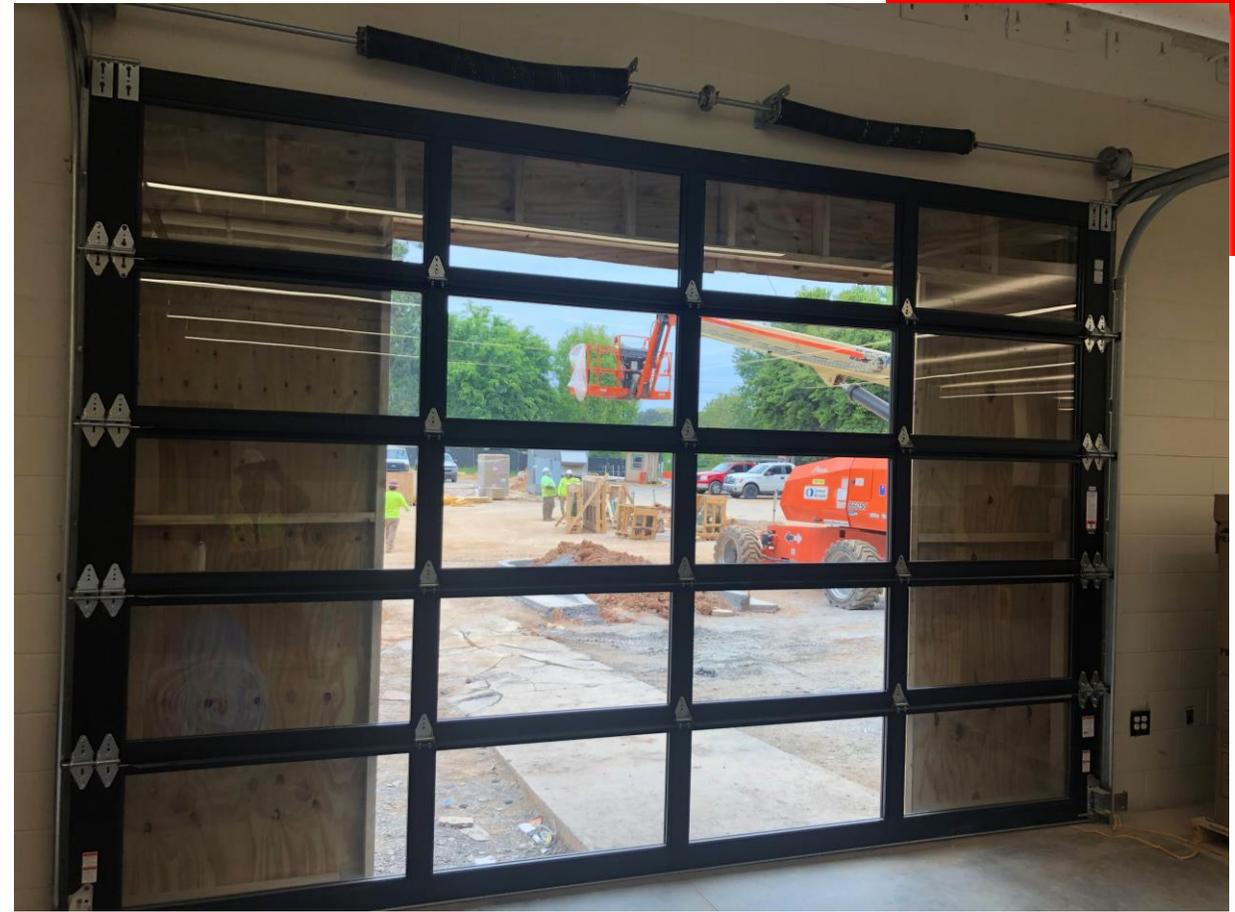

Sectional Doors Installed at New Addition



Photo Updates

East Elevation Hardscape Progress



Ceiling Tiles Installed, and MEP Trim Out Complete First Floor

