



Weekly Construction Progress Report

Grady High School

Week Ending: 5/22/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Parrish has continued to take measures to comply with the CDC and OSHA recommendations to keep the jobsite safe
- Poured remainder of South Wall at new addition building
- Remove old Mechanical Units
- MEP rough-in above ceiling and on Roof
- Remove ACT Ceilings in classrooms
- Continue tear off and replacement of Theater Building Roof
- Continuing TPO Install on 8th Street Building
- Waterproof elevator pit
- Completed flashing and weep hole installation at theater wall
- Completed Epoxy installation at 8th street group bathrooms
- Completed Foundation Block
- Began underground plumbing at new addition

NEXT WEEK – 5.25.2020 – 5.29.2020

- MEP rough-in above ceiling and on Roof
- Begin installing Water Source Heat Pumps in select areas
- Continue TPO Roof install at 8th street and Theater buildings
- Begin Epoxy in 8th Street Bathrooms
- Continue Masonry Restoration
- Demo ACT ceilings in classrooms in 8th Street
- Install storm and sewer lines for new addition
- Jack and Bore into manhole on 10th Street
- Waterproofing wall and installing foundation drainage system
- Begin Painting in Theater Building
- Ceramic Tile Installation in 8th Street Group Bathrooms



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 1,416,729.77

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG



Photo Updates

Installation of Theater and 8th Street Building Roof



Pouring remainder of concrete at South Wall of New Addition



Photo Updates

Remainder of South Wall of New Addition
being poured




Waterproofing Elevator Pit for New
Addition



Photo Updates

Removal of Existing Light Fixtures

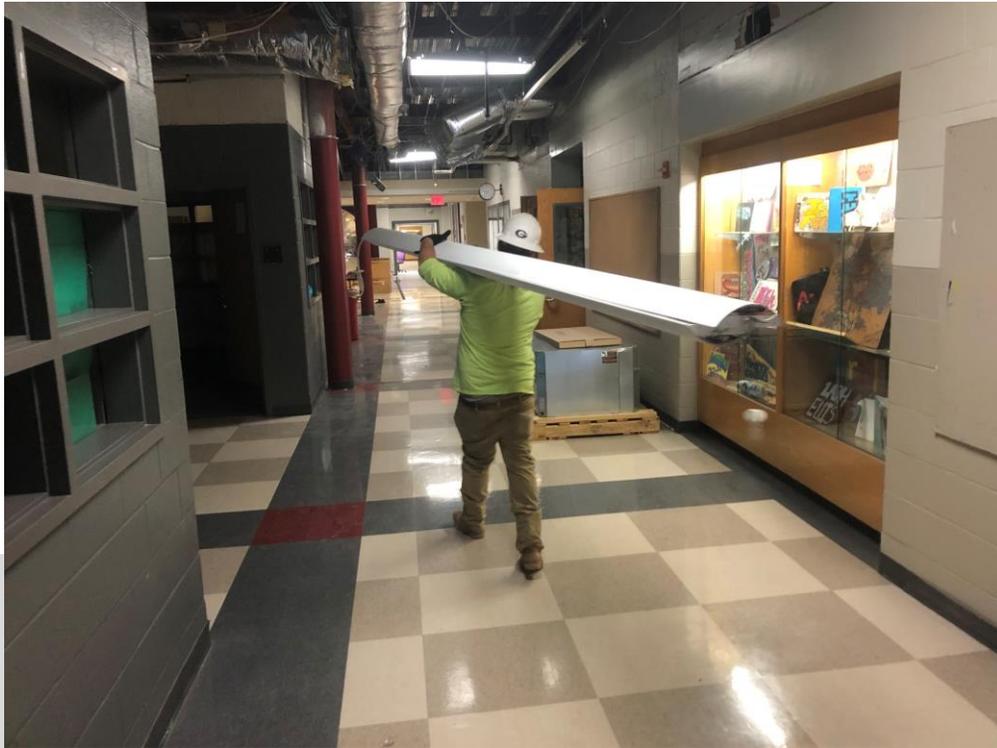


Old Water Source Heat Pumps Removed and New Water Source Heat Pumps Staged



Photo Updates

Scaffolding installed on East side of Charles Allen Building

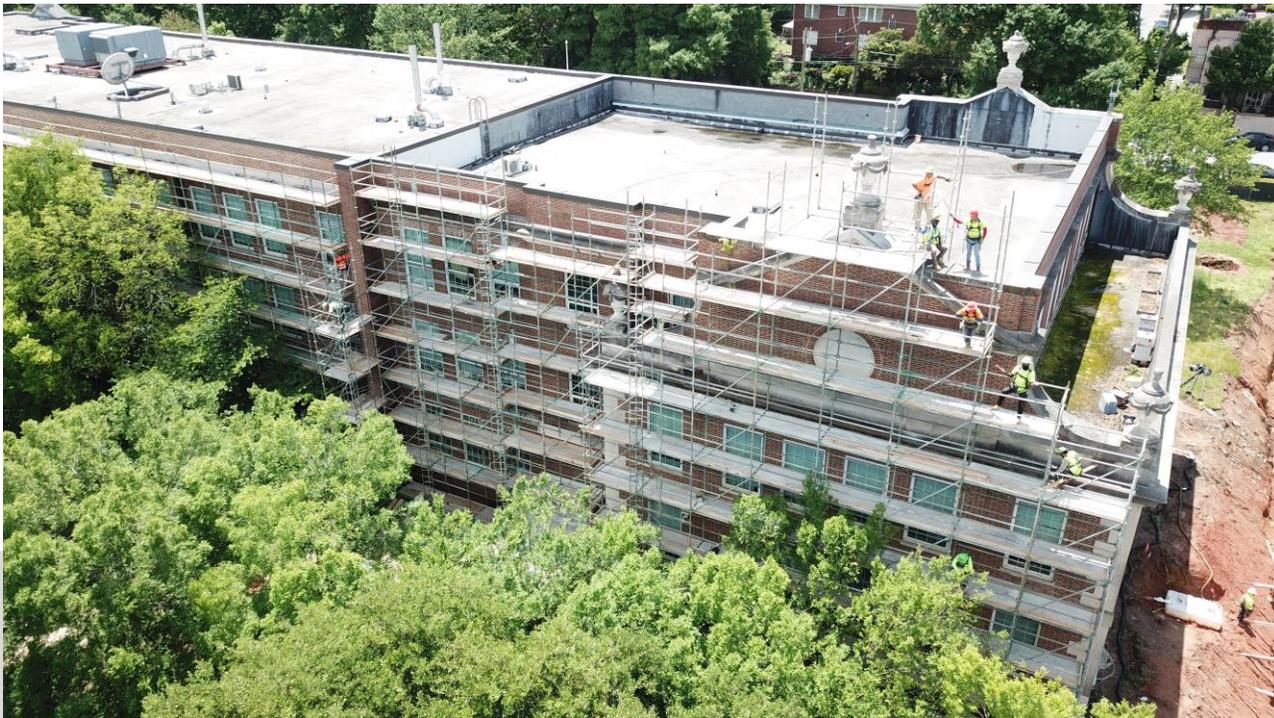

Removal of Ceiling Tile in classrooms



Photo Updates

Existing HVAC Units removed from 8th Street



Epoxy Flooring complete in 8th Street Building Group Bathrooms

