



Weekly Construction Progress Report

Grady High School

Week Ending: 11/06/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP overhead on Second floor of new addition.
- MEP overhead on Third floor of new addition.
- Continue CMU install Third Floor of new addition.
- Continue Fire Sprinkler Third Floor.
- Steel Erection for Bridge Connection with Charles Allen Building.
- Installed Stairwell 1 on East side of New Addition.
- Plumbing Rough-in third and fourth floor.
- Continued exterior metal framing.
- Install TPO Roof system at high roof of new addition.
- Interior Metal Framing 2nd Floor.
- Drywall Ceiling Framing 2nd Floor
- Began Brick Install at SE Corner.
- Firestopping First and Second Floor of New Addition.

NEXT WEEK – 11.09.2020 – 11.13.2020

- Continue CMU walls on the third floor of the new addition.
- Continue MEP overhead and rough-in on First, Second, Third, and Fourth floors of the new addition.
- Complete steel Erection for Bridge Connection with Charles Allen Building.
- Continue brick Install SE Corner.
- Continue interior and exterior metal framing.
- Complete TPO Roofing at new addition.
- Pour Concrete Landings and Treads at Stairwell 1.
- Continue Exterior Sheathing and Waterproofing at New Addition.
- Continue Firestopping First and Second Floor of New Addition.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 17,406,598.10

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG



Photo Updates

New Addition Progress



New Addition Progress



Photo Updates

Roofing Progress at New Addition




North Elevation View at New Addition



Photo Updates



Stairwell 1 Progress at New Addition

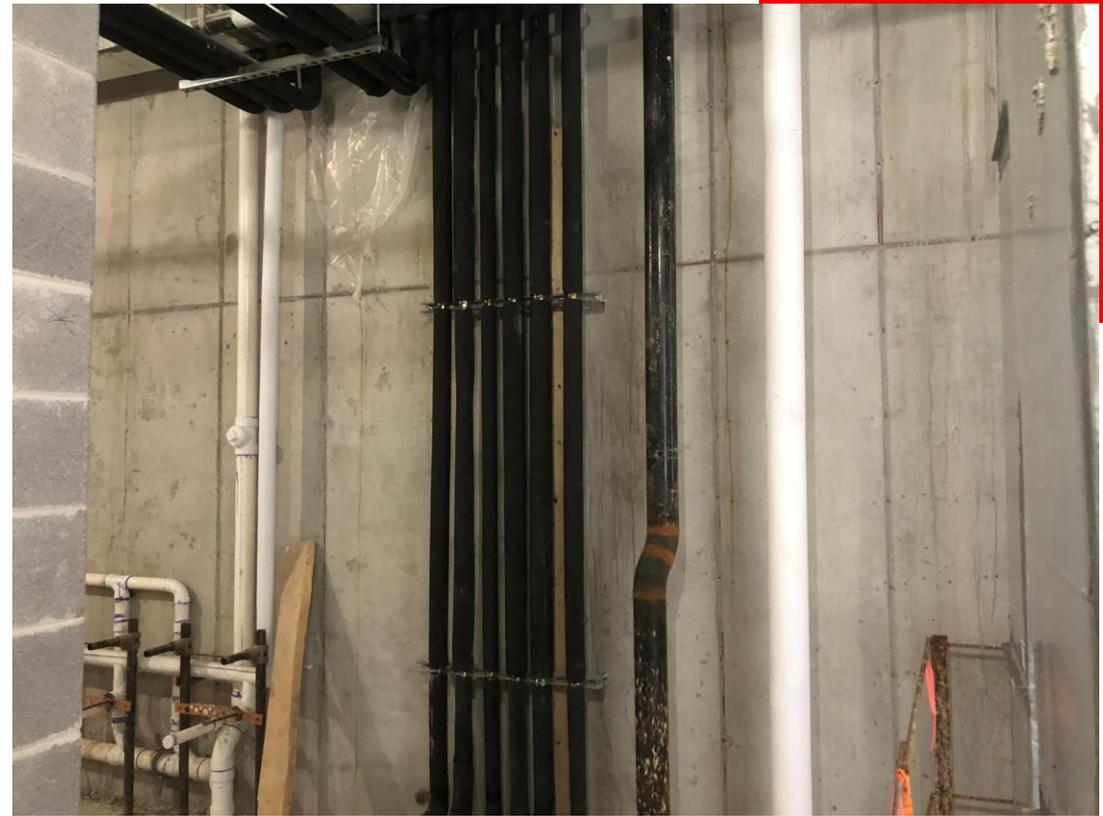

MEP Rough-In Progress at New Addition



Photo Updates

Drywall Ceiling Framed at Shop Space



2nd Floor Interior Metal Stud Framing Progress



Photo Updates

New TPO Roof Progress at New Addition



Interior Framing Second Floor of New Addition

