



Description

New Sod Planted Around Flagpole - East Parking

Taken Date

06/05/2025 at 12:36 pm

Uploaded By

Avery Hardeman

Upload Date

06/05/2025 at 12:38 pm

File Name

[86A1637F-6B91-48EC-9964-1E8...](#)

Album

Daily Logs



Description

Partitions Installed in Area A Boys Restroom

Taken Date

06/04/2025 at 02:31 pm

Uploaded By

Avery Hardeman

Upload Date

06/05/2025 at 12:37 pm

File Name

[79061CF8-7CE7-4D91-BA35-F15...](#)

Album

Daily Logs



Description

Sinks Installed in Area C Boys Restroom

Taken Date

06/02/2025 at 11:49 am

Uploaded By

Avery Hardeman

Upload Date


06/05/2025 at 12:37 pm

File Name

[22788BD6-D9DB-4BAE-A9DC-8E...](#)

Album

Daily Logs

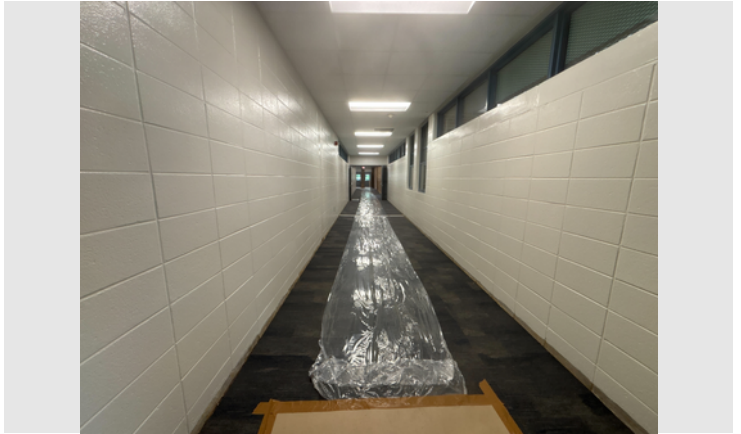

Description

Carpet Installed in Area D to E Hallway

Taken Date

06/02/2025 at 07:38 am

Uploaded By

Kasey Sterling

Upload Date

06/02/2025 at 07:38 am

File Name

[DF74CB9F-44D3-49B4-BEEF-C9E...](#)

Album

Daily Logs



Description

Carpet Installed in Area D

Taken Date

06/06/2025 at 08:17 am

Uploaded By

Kasey Sterling

Upload Date

06/06/2025 at 08:34 am

File Name

[2712F745-F217-4676-AC2A-AFB4...](#)

Album

Daily Logs



Description

Toilets Installed Area B Girls Restroom

Taken Date

06/04/2025 at 02:33 pm

Uploaded By

Avery Hardeman

Upload Date

06/05/2025 at 07:34 am

File Name

[272BCA2E-0E77-482A-AA74-779...](#)

Album

Daily Logs



Description

Carpet Installed in Area C

Taken Date

06/04/2025 at 12:30 pm

Uploaded By

Avery Hardeman

Upload Date

06/05/2025 at 12:37 pm

File Name

[F65C7856-6186-4E46-A878-CED...](#)

Album

Daily Logs



Description

New Sod Planted - East Parking

Taken Date

06/04/2025 at 08:54 am

Uploaded By

Kasey Sterling

Upload Date

06/04/2025 at 08:55 am

File Name

[EB426491-667B-4EC0-96C2-B21...](#)

Album

Daily Logs

WEEKLY PROGRESS UPDATE REPORT

KIPP Vision Elementary

06/02/25 – 06/06/25



Last Week's Activities:

- Start tile – Area D
- Start landscaping – East Parking
- Start plumbing fixture installation – All Areas
- Continue paint – All Areas
- Complete light installation and motion sensors – All Areas
- Complete restroom heaters – Area B
- Complete HVAC trim outs – All Areas
- Complete restroom doors and hardware installation – All Areas
- Complete concrete pad installation – Flagpole

This Week's Activities:

- Start classroom cleaning – All Areas
- Start carpet installation – Area B
- Start exterior painting – Bus Lane
- Complete carpet installation – Area A
- Complete carpet installation – Area C
- Complete partition installation – Area A
- Complete interior paint – All Areas
- Complete sod – Flagpole
- Complete sod – East Parking
- Complete gas line installation – Area B
- Complete toilet fixture and sensor install – Area A
- Complete toilet fixture and sensor install – Area B
- Complete toilet fixture and sensor install – Area C
- Complete handrail installation – Courtyard

Next Week's Activities:

- Start base install – All Areas
- Start masonry brick wall – Dumpster Enclosure
- Start accessories installation – Area A
- Start accessories installation – Area C
- Start ornamental fence installation – East Parking
- Start storage room epoxy floor install – Area B and D
- Start epoxy floor install – Area D
- Continue carpet installation – Area A
- Continue carpet installation – Area B
- Continue cleaning – All Areas

WEEKLY PROGRESS UPDATE REPORT

KIPP Vision Elementary

06/02/25 – 06/06/25



<u>Contract and Billings</u>	
Contract	
Current Contract Value	\$6,040,748.16
Billings	
Date Last Billing Submitted	4/30/2025
Total Billed to Date (Including Retainage)	\$3,929,866
Date of Last Payment	04/08/2025
Amount Paid to Date	\$1,137,867
Amount Open Receivables (Not Including Retainage)	\$2,598,506
Percent Billed to Date	65%
