


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit Center

WEEK ENDING 01/05/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LA MONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

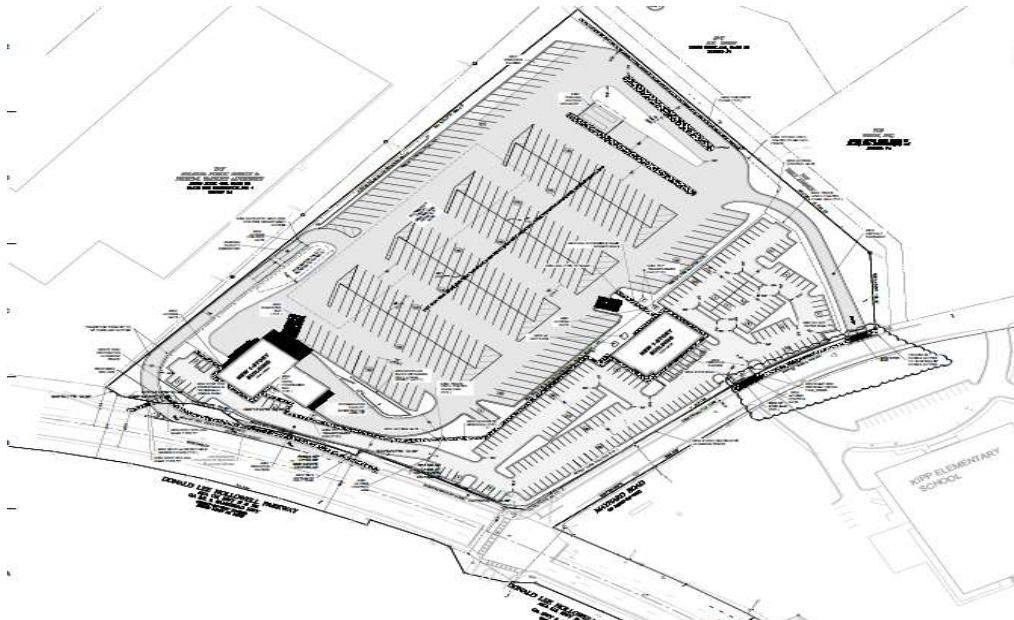

WEEKLY CONSTRUCTION PROGRESS REPORT



Construction Activities this week

- 100% OF CMP HAS BEEN SET IN THE RETENTION POND. TASK IS COMPLETED.
- SITE CONTRACTOR IS IN THE PROCESS OF THE OCS (OUTLET CONTROL STRUCTURE) TIE IN TO THE POND.
- 80% COMPLETED WITH STORM LINES/STRUCTURES.
- 100% COMPLETED WITH OPERATIONS BUILDING PAD.
- 100% COMPLETED WITH MAINTENANCE BUILDING PAD. GRAVEL NEEDS TO BE LAID.
- SS BORE ACROSS MAYNARD STREET TO CONDUCT WEEK OF (01/08/24). JACK & BORE CREW WILL MOBILIZE EARLY NEXT WEEK.
- UNDERGROUND RETENTION SITE PREP.
- 100% OF MASS GRADING FOR LAYDOWN AREA IS COMPLETE. GRAVEL NEEDS TO BE LAID. EQUIPMENT AND CONEX BOXES HAVE ARRIVED ONSITE.
- FIRE RISER DELIVERED ONSITE (01/03/24).

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON BUILDING PERMIT STATUS AND WEATHER.

- CONCRETE, REBAR, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES WILL CONTINUE WEEK OF (01/08/24)
- STRUCTURAL FOUNDATION LAYOUT
- UNDERSLAB PLUMBING INSTALLATION (MEP INSTALLATION) WILL COMMENCE WEEK OF (01/08/24)
- CONCRETE WORK/POUR SLABS
- SEWER LINES WILL BEGIN TO BE INSTALLED WEEK OF (01/08/24).
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.

MANPOWER LOG (WEEK OF 01/05/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	12	15	16	16	15

WEATHER LOG (MONTH OF DECEMBER/JANUARY)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (9) NINE TRACKED RAIN DAYS IN DECEMBER.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23)
- AVERAGE RECOVERY TIME: 2-3 DAYS
- NO RAIN TO REPORT FOR WEEK OF (01-05-24).

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

