


Quote of the week: "Let the beauty of what you love be what you do."

Project: FL Stanton ES Renovation and addition

Week November 17, 2023

- Continued electrical rough-in overhead on all 3 levels
- Continue electrical wall rough in on the lower level and level 1
- Began electrical rough-in at the gym
- Completed Framing exterior stud walls @ 1958 lower level
- Completed sheathing on exterior walls @ 1958 wing
- Completed framing furr out walls in the 1928 wing
- Started plumbing overhead rough - in
- Began hanging VRF Cassettes
- Begin demo of sanitary sewer lines at new kitchen - addition
- Installed new coping, gutters and downspouts
- Installed roof and overflow drains

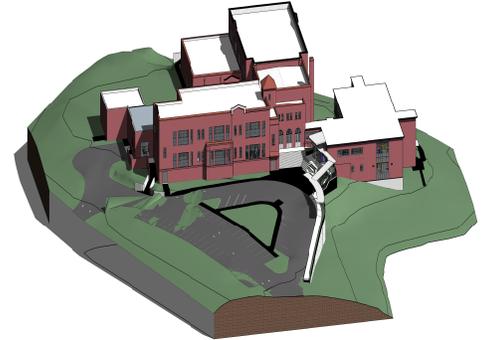

Continue to installing Sheathing at the 1928 building



Removing and Relocating Sanitary Sewer lines to begin kitchen addition building pad.



Continue interior furring wall install



In route to begin underground trench pour back

NEXT WEEK – November 20 - November 24

- Continue electrical rough in below ceilings
- Began framing walls at stem classroom
- Begin framing walls at the new media center
- Begin installing roof curbs
- Hang duct on the lower level
- Begin masonry Infilling and tooting
- Begin plumbing trench pour backs
- Complete VRF install throughout
- Begin Pipe installation for VRF cassettes
- Begin roofing around roof drains and overflows
- Complete terracotta tile reinstall
- complete grading for new building pad - Kitchen Addition

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
