



# **Weekly Construction Progress Report**

**Midtown High School**

**Week Ending: 2/12/2021**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## THIS WEEK

- MEP overhead on second, third and fourth floor of new addition.
- Continue fire sprinkler third floor and Stair 1 Riser.
- Firestopping Fourth Floor of New Addition.
- Waterproofing complete on North, and West side of new addition.
- Grading East elevation in preparation for Hardscapes.
- Continue brick install at North and South elevations.
- Continue Brick Installation at Patio Roof.
- Install cast stone windowsills and Parapet Caps.
- Cleaning of Brick at South Elevation.
- Continue Installing Windows at South Elevation.
- Fireproofing at new addition bridge.
- Began installing Curtainwall at East Elevation.
- Install Handwash station in 8<sup>th</sup> street building cafeteria.
- Begin fire sprinkler install on 4<sup>th</sup> floor of new addition.

## NEXT WEEK – 2.15.2021 – 2.19.2021

- Continue MEP overhead and rough-in on Second, Third, and Fourth floors of the new addition.
- Setting HVAC units on New Addition Building.
- Complete red brick install at North and South elevations.
- Continue interior metal framing.
- Continue firestopping fourth floor of new addition.
- Acoustical Ceiling Grid install Second Floor of New Addition.
- Continue installing curtainwall on East Elevation.
- Installing light and Low-Voltage fixtures.
- Installing Windows at South Elevation of New Addition.
- Continue preparing for hardscapes on East Elevation.



# Budget & Schedule

## BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 24,746,340.44

## SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



## ADDITIONAL INFO

- Scheduled Substantial Completion Date
  - July 29, 2021
- Completed By
  - Will Henry, PCG
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Katy Daugharty, CC
  - Bob Just, CC
  - Jim Fallon, PCG
  - Alex Johnson, PCG
  - Will Henry, PCG
  - Art Cofelice, PCG
  - Travis Disbro, PCG
  - Tyler Cobb, PCG
  - Paul Cobb, PCG



# Photo Updates

New Addition Progress – South Elevation




New Addition Progress – North Elevation



# Photo Updates

East Elevation Brick Completed

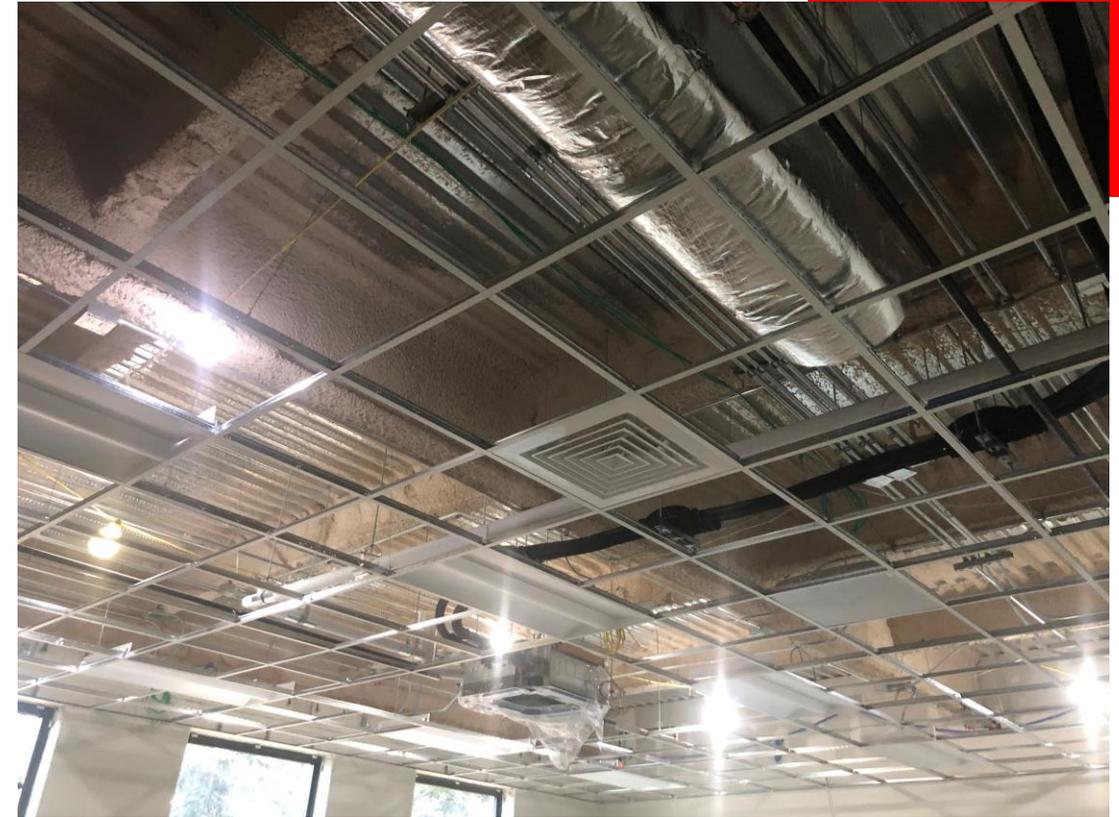

First Floor Classroom Progress



# Photo Updates

Metal Doors Installed at New Addition  
Electrical Rooms



East Elevation of New Addition Being  
Prepared for Hardscapes



# Photo Updates

MEP Overhead Progress



4<sup>th</sup> Floor Group Restroom Progress

