



Weekly Construction Progress Report

Midtown High School

Week Ending: 2/26/2021

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP overhead on second, third and fourth floor of new addition.
- Firestopping Fourth Floor of New Addition.
- Poured Concrete foundations for switchback ramp on East Elevation.
- Continue brick install at West elevations.
- Complete Brick Installation at Patio Roof.
- Install cast stone windowsills and Parapet Caps.
- Cleaning of Brick at South and North Elevation.
- Continue Installing Windows at South Elevation.
- Completed installing Curtainwall framing at East Elevation.
- Begin Storefront Installation at South Elevation of New Addition.
- Continue fire sprinkler install on 4th floor of new addition.
- Complete red brick install at South elevations.

NEXT WEEK – 3.01.2021 – 3.05.2021

- Continue MEP overhead and rough-in on Second, Third, and Fourth floors of the new addition.
- Setting HVAC units on New Addition Building (March 3).
- Continue Red brick install at West Elevations.
- Continue interior metal framing and Gypsum Board Install.
- Continue firestopping fourth floor of new addition.
- Acoustical Ceiling Grid install Second Floor of New Addition.
- Installing light and Low-Voltage fixtures.
- Installing Storefront at South Elevation of New Addition.
- Continue preparing for hardscapes on East Elevation.
- Pour Concrete Walls at East Elevation Hardscapes.
- Begin Metal Panel Installation



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 26,463,871.02

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG
 - Tyler Cobb, PCG
 - Paul Cobb, PCG



Photo Updates

New Addition Progress – West Elevation



New Addition Progress – North Elevation



Photo Updates

Installing High Impact Gypsum Board on
Media Center Metal Stud Walls



Gypsum Board Installed in New Addition
Media Center



Photo Updates

South Elevation Window Progress




South Elevation Window Progress



Photo Updates

East Elevation Hardscape Progress

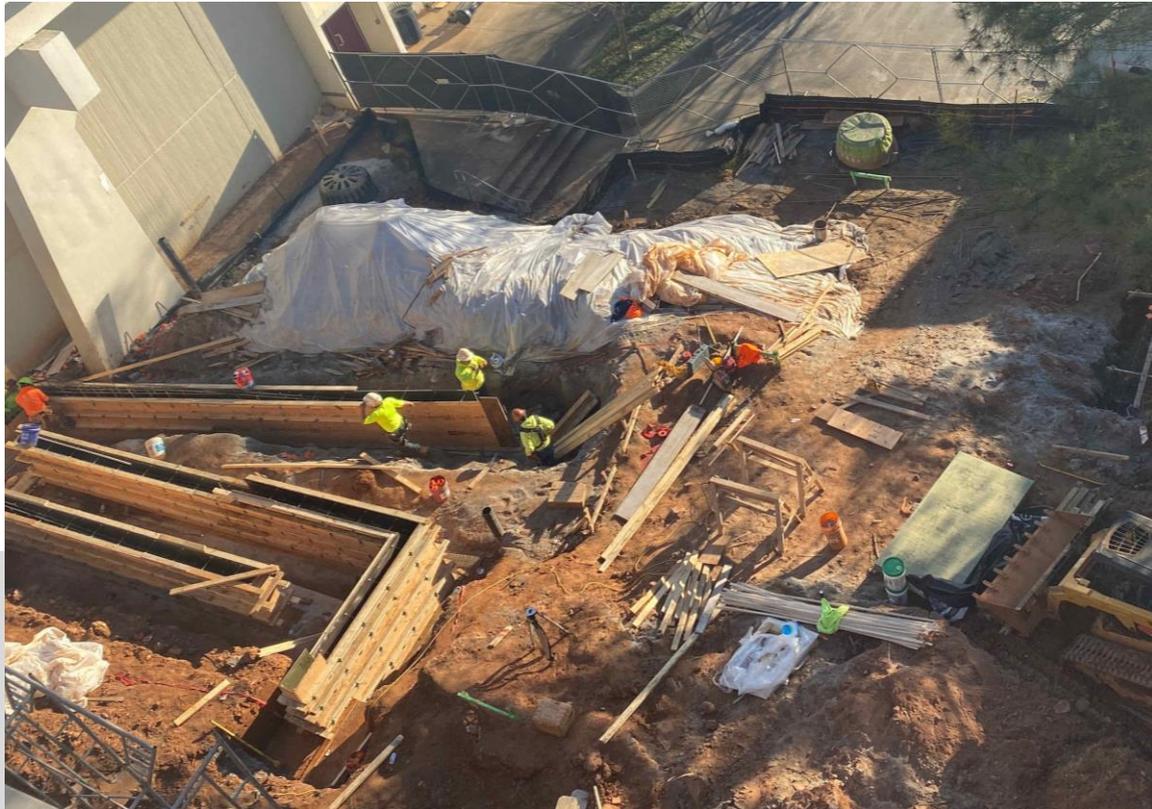


Patio Brick and Cast Stone Progress



Photo Updates

New Addition East Elevation Progress

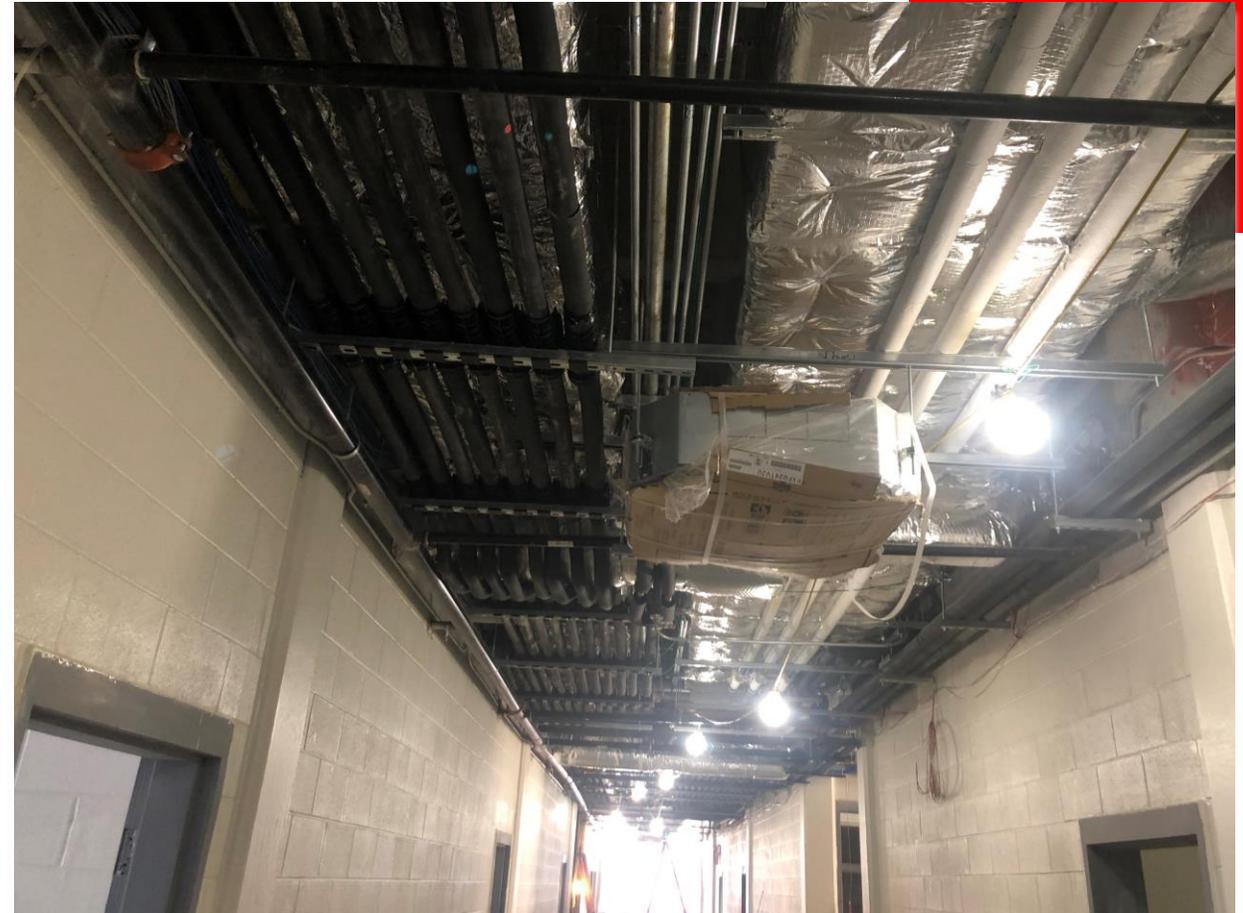

MEP Overhead Progress

