



Weekly Construction Progress Report

**Midtown High School
Week Ending: 5/7/2021**

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP startup and trim out in new addition building.
- Continue fire sprinkler on 4th floor of new addition.
- Continue Metal Panel Installation at New Addition.
- Continue Patio Roofing system.
- Continue hardscapes on the North Elevations.
- Continue VCT and flooring finishes in New Addition Building.
- Completed Terrazzo Installation on Second Floor of New Addition Building.
- Continue Multipurpose and CTAE build back in 8th street building.
- Dropping ceiling tiles in New Addition Building.
- Begin Curtainwall Installation at New Addition and C. Allen Building Bridge.
- Charles Allen building Administration Demolition to prepare for Terrazzo flooring.

NEXT WEEK – 5.10.2021 – 5.14.2021

- Continue MEP Startup and trim out in the New Addition Building.
- Installing lights and Low-Voltage fixtures.
- Continue hardscapes on the North and South Elevations.
- Continue Patio Roofing system.
- Continue Metal Panel Installation.
- Complete Epoxy flooring in New Addition Restrooms.
- Continue VCT and Flooring Finishes in new Addition Building.
- Continue Curtainwall Installation at New Addition and C. Allen Building Bridge.
- Begin Canopy Install on East Elevation.
- Pour Foundations for Granite Walls on South Elevation.
- Begin installing glass at New Addition Bridge Curtainwall.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 29,378,364.35

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG
 - Tyler Cobb, PCG
 - Paul Cobb, PCG



Photo Updates

Terrazzo Installed on Second Floor of New Addition Building



Casework Installed in Science Labs in New Addition Building



Photo Updates

Curtainwall Frames Installed at New Addition Bridge




Demolition Complete for New Door Opening for New Reception Area in Charles Allen Building



Photo Updates

Patio Paver Progress at New Addition Building

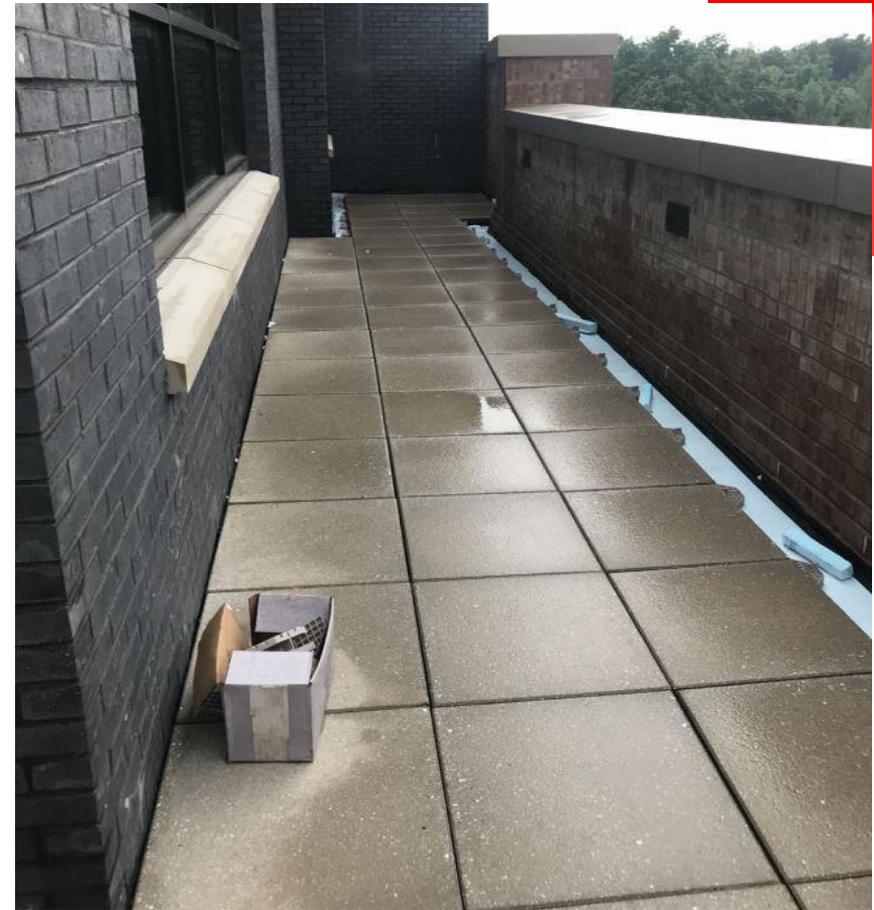

Patio Paver Progress at New Addition Building

