



# Weekly Construction Progress Report

**Grady High School**

**Week Ending: 6/26/2020**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## THIS WEEK

- Continue MEP rough-in above ceiling and on Roofs.
- Installing Toilet Accessories in 8<sup>th</sup> Street Bathrooms.
- Continue rough in for HVAC Controls.
- Continue Practice Gym Roof and Begin Performance Gym Roof.
- Complete Epoxy in 8<sup>th</sup> Street Single Bathrooms.
- Continue Masonry Restoration & Waterproofing.
- Underground electrical for new addition.
- Painting Theater cloud ceilings.
- Continue Grading Parking Lot.
- Begin Demo in Performance Gym Lobby.
- Paint 8<sup>th</sup> Street Building Classrooms and Corridors
- Curb and Gutter at Parking lot for new addition
- First Floor Slab Prep

## NEXT WEEK – 6.29.2020 – 7.03.2020

- Continue MEP rough-in above ceiling and on Roof.
- Continue rough in for HVAC Controls.
- Continue TPO Roof install at 8<sup>th</sup> street and Practice Gym Roof.
- Begin Cove Base Install
- Continue Masonry Restoration & Waterproofing.
- Pour First floor Slab at New Addition
- Painting 8<sup>th</sup> Street Building classrooms.
- Demo Performance Gym Masonry Walls and Finishes
- Begin Ceiling Grid install in 8<sup>th</sup> Street Classrooms
- Complete Painting in 8<sup>th</sup> Street Building
- Begin Lighting reinstallation
- Begin Paving Parking Lot end of the week



# Budget & Schedule

## BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 3,808,514.49

## SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



## ADDITIONAL INFO

- Scheduled Substantial Completion Date
  - July 29, 2021
- Completed By
  - Alex Johnson, PCG
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Katy Daugharty, CC
  - Bob Just, CC
  - John Rood, PCG
  - Darrell Bailey, PCG
  - Alex Johnson, PCG
  - Will Henry, PCG
  - Art Cofelice, PCG



# Photo Updates

Site Overview



First Floor of New Addition Slab Prep



# Photo Updates

Curb and Gutter being installed at New Addition Parking Lot




Installing Underground Electrical at New Addition



# Photo Updates

Basement Steel Primed and Painted

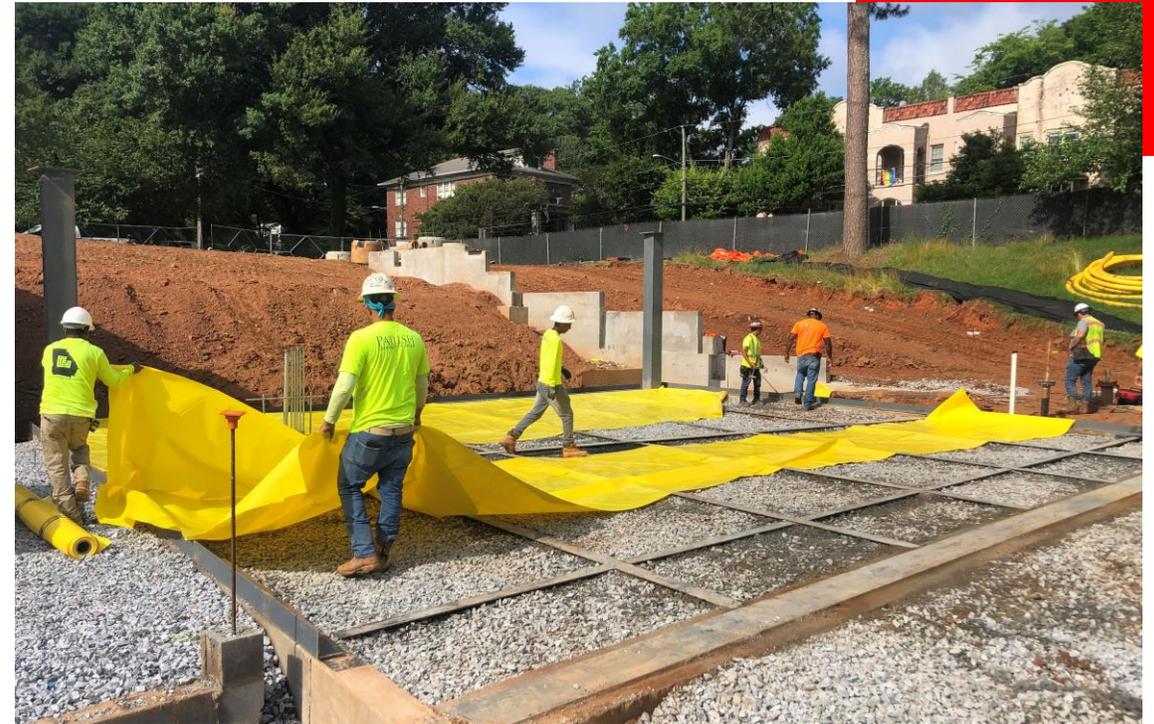


Installing Vapor Barrier at basement of  
New Addition Building



# Photo Updates

Decking installed in New Addition Basement

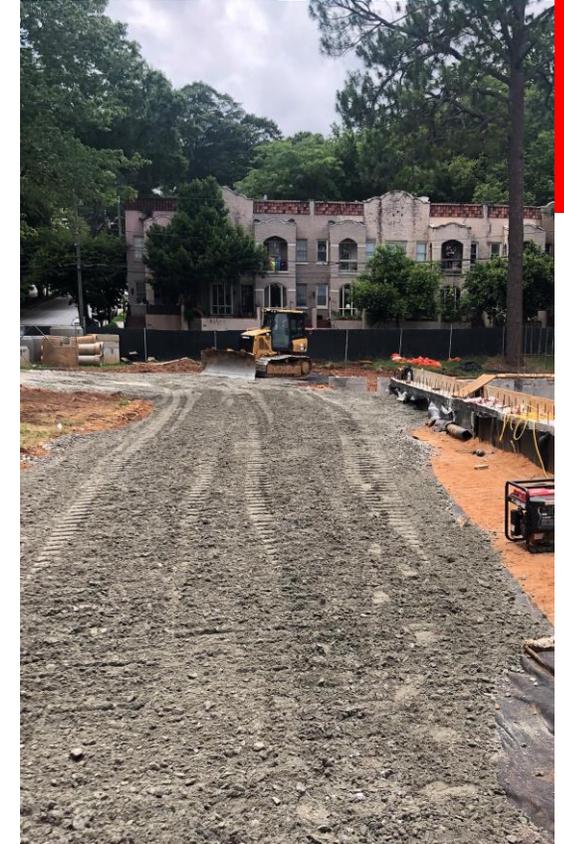

Backfill of South Foundation Wall complete



# Photo Updates

## Overall Summer 2020 Roofing Progress



Toilet Partitions completed in 8<sup>th</sup> Street Building

