



# **Weekly Construction Progress Report**

**Grady High School**

**Week Ending: 11/20/2020**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## THIS WEEK

- MEP overhead on Second floor of new addition.
- MEP overhead on Third floor of new addition.
- Completed CMU install Third Floor of new addition.
- Continue Fire Sprinkler Third Floor.
- Stair 2 Erection
- Plumbing Rough-in third and fourth floor.
- Continued exterior metal framing and sheathing.
- Complete Spray Fireproofing Fourth Floor of New Addition.
- Granite Installation beginning at North East Elevation
- Interior Metal Framing 2<sup>nd</sup> Floor.
- Continue Brick Install at South and East Corner.
- Firestopping First and Second Floor of New Addition.
- Spray foam acoustical insulation installed in Shop Space
- Waterproofing applied on North, and West side of new addition.

## NEXT WEEK – 11.23.2020 – 11.25.2020

- Begin CMU walls on the fourth floor of the new addition.
- Continue MEP overhead and rough-in on First, Second, Third, and Fourth floors of the new addition.
- Continue brick Install South and East Corner.
- Continue Waterproofing at New Addition.
- Continue interior and exterior metal framing.
- Continue Exterior Sheathing and Waterproofing at New Addition.
- Continue Firestopping First and Second Floor of New Addition.
- Continue granite Installation beginning at North Elevation.



# Budget & Schedule

## BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 17,406,598.10

## SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



## ADDITIONAL INFO

- Scheduled Substantial Completion Date
  - July 29, 2021
- Completed By
  - Will Henry, PCG
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Katy Daugharty, CC
  - Bob Just, CC
  - Jim Fallon, PCG
  - Darrell Bailey, PCG
  - Alex Johnson, PCG
  - Will Henry, PCG
  - Art Cofelice, PCG
  - Travis Disbro, PCG



# Photo Updates

New Addition Progress



New Addition Progress



# Photo Updates

New Exhaust Fans Installed at New Addition Roof



New TPO Roof Installed at New Addition and Rooftop Curbs Set for new HVAC Units



# Photo Updates

Red Brick Progress at South East Corner




Black Brick and Granite Progress at North East Corner



# Photo Updates

Exterior Sheathing installed at New Addition Media Center Wall

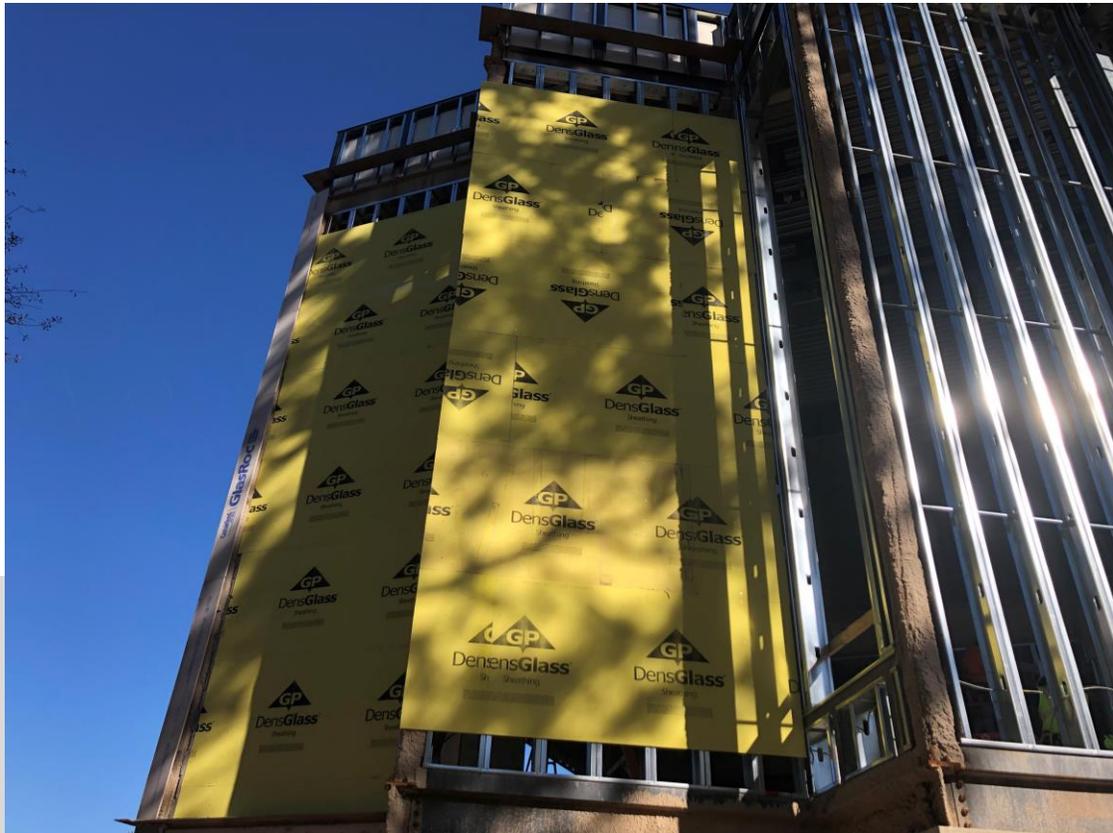

Exterior Sheathing Completed at South Side of New Addition



# Photo Updates



Stairwell 2 Installation Progress



Fireproofing Progress at 4<sup>th</sup> Floor  
of New Addition

