



# Weekly Construction Progress Report

**Grady High School**

**Week Ending: 12/18/2020**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## THIS WEEK

- MEP overhead on Second floor of new addition.
- MEP overhead on Third floor of new addition.
- Continue CMU walls on the fourth floor of the new addition.
- Continue Fire Sprinkler Third Floor.
- Plumbing Rough-in fourth floor.
- Continued exterior metal framing and sheathing.
- Granite Installation at North Elevation
- Hang, Tape, and Finish Gypsum Board
- Continue Brick Install at South and East Corner of New Addition.
- Firestopping Second, and Third Floor of New Addition.
- Waterproofing applied on North, and West side of new addition.
- Blockfill Third Floor of New Addition.
- Completed tie-in Fire Meter Vault and Hydrant off C. Allen Drive.
- Begin TPO Roof at Bridge, Stair 1, and C. Allen building Low Roof.

## NEXT WEEK – 12.21.2020 – 12.25.2020

- Complete CMU walls on the fourth floor of the new addition.
- Continue MEP overhead and rough-in on Second, Third, and Fourth floors of the new addition.
- Continue brick Install South and East Corner.
- Continue Waterproofing at New Addition.
- Continue interior and exterior metal framing.
- Continue Exterior Sheathing and Waterproofing at New Addition.
- Continue Firestopping Second and Third Floor of New Addition.
- Continue granite Installation at West Elevation.
- Continue Installing Gypsum Board on First and Second Floor of New Addition.
- Continue TPO Roof at Bridge, Stair 1, and Charles Allen Building Low Roof.



# Budget & Schedule

## BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 20,122,064.79

## SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



## ADDITIONAL INFO

- Scheduled Substantial Completion Date
  - July 29, 2021
- Completed By
  - Will Henry, PCG
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Katy Daugharty, CC
  - Bob Just, CC
  - Jim Fallon, PCG
  - Darrell Bailey, PCG
  - Alex Johnson, PCG
  - Will Henry, PCG
  - Art Cofelice, PCG
  - Travis Disbro, PCG



# Photo Updates

New Addition Progress – North Elevation



New Addition Progress – South Elevation



# Photo Updates

## Switchgear Installed in Main Electrical Room



## Transfer Switches and Electrical Panels Installed



# Photo Updates

Metal Framing Progress in Media Center




Gypsum Board Wall Progress 1<sup>st</sup> Floor of New Addition



# Photo Updates

Counseling Office Progress

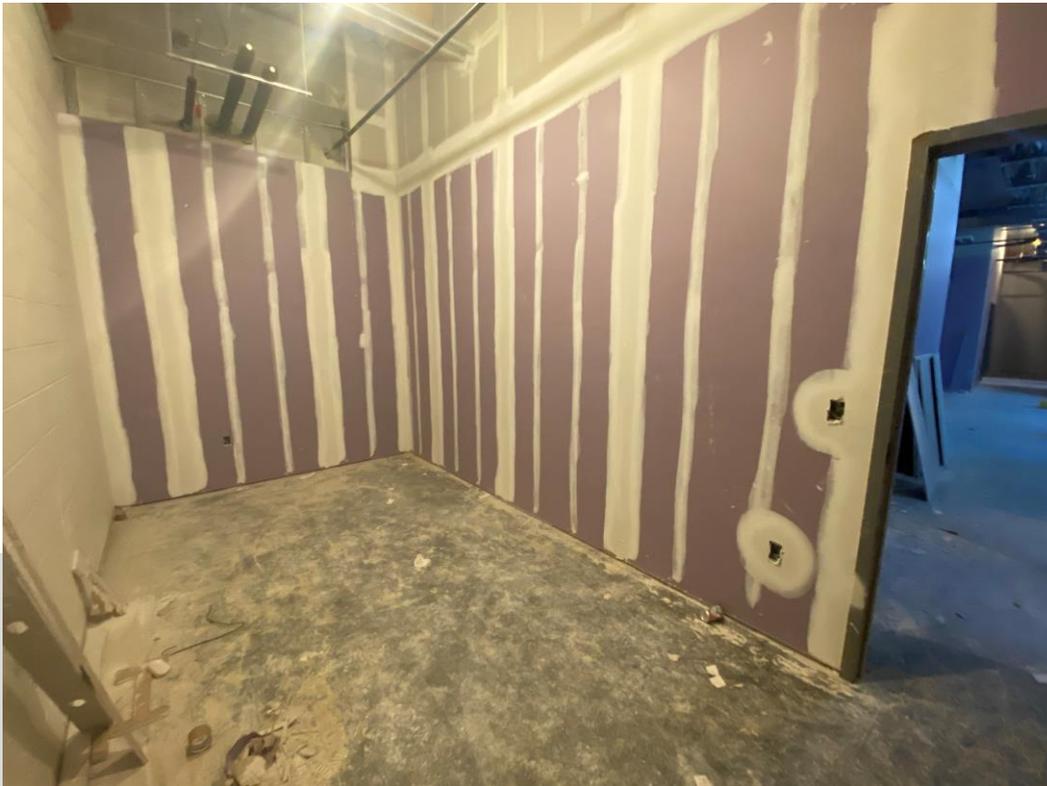

Counseling Area Progress



# Photo Updates



Metal Framing Progress in Restroom



Block fill Completed on 3<sup>rd</sup> Floor of  
New Addition

