



Weekly Construction Progress Report

Grady High School

Week Ending: 5/1/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Parrish has continued to take measures to comply with the CDC and OSHA recommendations to keep the jobsite safe
- Completed reroute of Fire and Water Lines to remove them from building pad
- Completion of Geopier System
- Began digging foundations on South and West Walls of new addition
- Began refacing CMU Block in group restrooms for new ceramic tiles.
- Pour New Addition, South and South West Wall Foundations on Friday 5/01
- Grady High School Teachers have begun moving out of their classrooms

NEXT WEEK – 5.04.2020 – 5.08.2020

- Install Stormwater Detention System
- Begin underground plumbing
- Relocating existing Gas Line to avoid building pad
- Continue to dig Foundations on the West side of the new addition
- Begin installing scaffolding for Masonry Restoration at Charles Allen Building
- Parrish Masonry will begin installing flashing and weep holes to existing brick at Theater Wall
- MEP rough-in above ceiling and on Roof
- Roofers Preinstall meeting and mobilization on 5/6
- Begin Tear off and replacement of Theater Roof 5/8, pending weather
- Grady High School Staff continues to move out of classrooms



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 1,416,729.77

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG



Photo Updates

Jobsite Overview



Geopier System complete



Photo Updates

Foundation at South Wall of New Addition



Progress of South Wall Foundation at New Addition



Photo Updates

Installation of Foundation Rebar on South Wall of New Addition




Overview of South and West Foundations at New Addition



Photo Updates

Rebar getting prepped for concrete Pour of South and West Foundations on 5/1

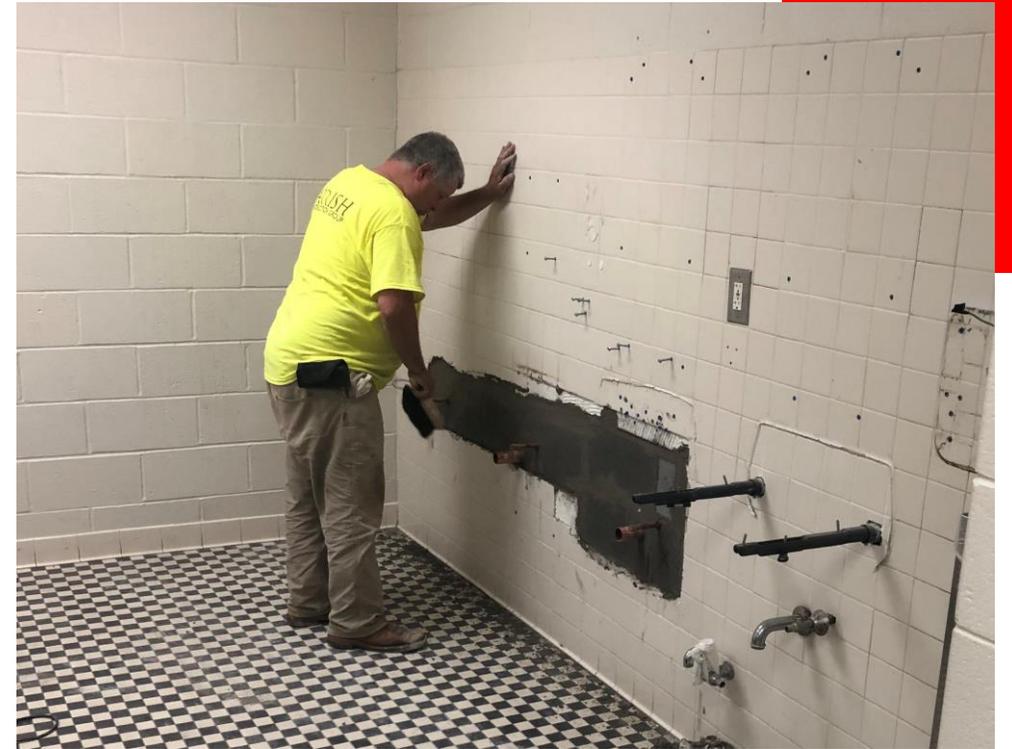

Mason Refacing Block in 8th Street Group Bathrooms for new Ceramic Wall Tile

