



# Weekly Construction Progress Report

**Midtown High School**

**Week Ending: 3/12/2021**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## THIS WEEK

- MEP overhead on second, third and fourth floor of new addition.
- Poured switchback ramp on East Elevation.
- Completed brick install at West elevations.
- Install cast stone Parapet Caps at Patio Roof.
- Cleaning of Brick at South and North Elevation.
- Begin Storefront frames and glazing Installation at North Elevation of New Addition.
- Continue fire sprinkler install on 4<sup>th</sup> floor of new addition.
- Continue Metal Panel Installation at South and West Elevation.
- Begin Elevator Installation.
- Began Hanging, Taping, and Finishing Group Bathrooms First and Second Floor.
- Acoustical Ceiling Grid install Second Floor of New Addition.
- Install Intumescent Paint in Stairwell 1.

## NEXT WEEK – 3.15.2021 – 3.19.2021

- Continue MEP overhead and rough-in on Second, Third, and Fourth floors of the new addition.
- Continue interior metal framing and Gypsum Board Install.
- Acoustical Ceiling Grid install Second Floor of New Addition.
- Installing lights and Low-Voltage fixtures.
- Installing Storefront frames at North Elevation of New Addition.
- Pour Concrete Stairs at East Elevation Hardscapes.
- Continue Elevator Installation.
- Complete North Elevation Glazing install.
- Begin Patio Roofing system.



# Budget & Schedule

## BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 26,463,871.02

## SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



## ADDITIONAL INFO

- Scheduled Substantial Completion Date
  - July 29, 2021
- Completed By
  - Will Henry, PCG
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Katy Daugharty, CC
  - Bob Just, CC
  - Jim Fallon, PCG
  - Alex Johnson, PCG
  - Will Henry, PCG
  - Art Cofelice, PCG
  - Travis Disbro, PCG
  - Tyler Cobb, PCG
  - Paul Cobb, PCG



# Photo Updates

New Addition Progress – West Elevation



New Addition Progress – North Elevation



# Photo Updates

Gypsum Board Progress at Lower Media Center Ceilings




Gypsum Board Progress in Group Restrooms



# Photo Updates

Metal Panel Progress South Elevation

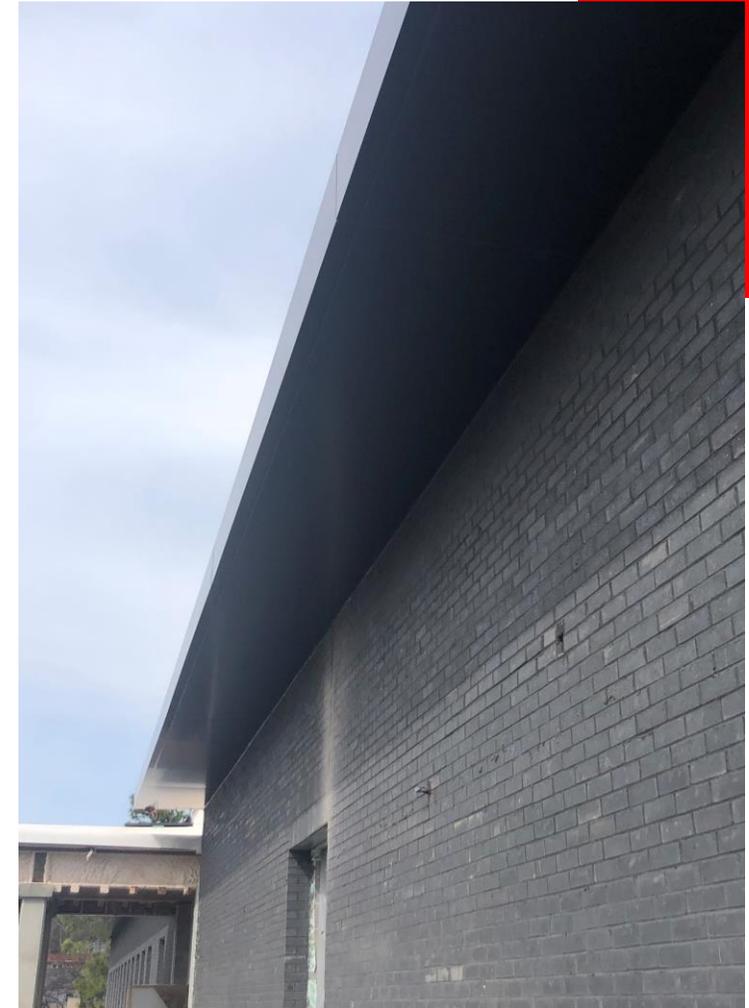

Metal Panel Progress  
South East Elevation



# Photo Updates

## Hardscape Progress East Elevation



## Hardscape Progress East Elevation



# Photo Updates

## North Elevation Grading Progress



## ACT Ceiling Progress 2<sup>nd</sup> Floor

