



Weekly Construction Progress Report

Midtown High School

Week Ending: 3/19/2021

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP overhead on third and fourth floor of new addition.
- Completed parapet cast stone at Patio elevations.
- Cleaning of Brick at South and North Elevation.
- Completed Storefront frames and glazing Installation at North Elevation of New Addition.
- Continue fire sprinkler install on 4th floor of new addition.
- Continue Metal Panel Installation at South and West Elevation.
- Continue Elevator Installation.
- Gypsum Board Finishing in Bathrooms and on Second Floor Media Center.
- Acoustical Ceiling Grid install Second Floor of New Addition.
- Completed Intumescent Paint in Stairwell 1.
- Pour Concrete Stairs at East Elevation Hardscapes.

NEXT WEEK – 3.22.2021 – 3.26.2021

- Continue MEP overhead and rough-in on Third, and Fourth floors of the new addition.
- Acoustical Ceiling Grid install Third Floor of New Addition.
- Installing lights and Low-Voltage fixtures.
- Continue hardscapes on the East and South East Elevations.
- Continue Elevator Installation.
- Continue Curtainwall installation on West Elevation.
- Begin Patio Roofing system.
- Begin Ceramic Tile Installation in Restrooms.
- Continue Metal Panel Installation.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 26,463,871.02

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG
 - Tyler Cobb, PCG
 - Paul Cobb, PCG



Photo Updates

Curtainwall Install at North West Elevation




New Addition Progress – North Elevation



Photo Updates

Hardscape Progress East Elevation

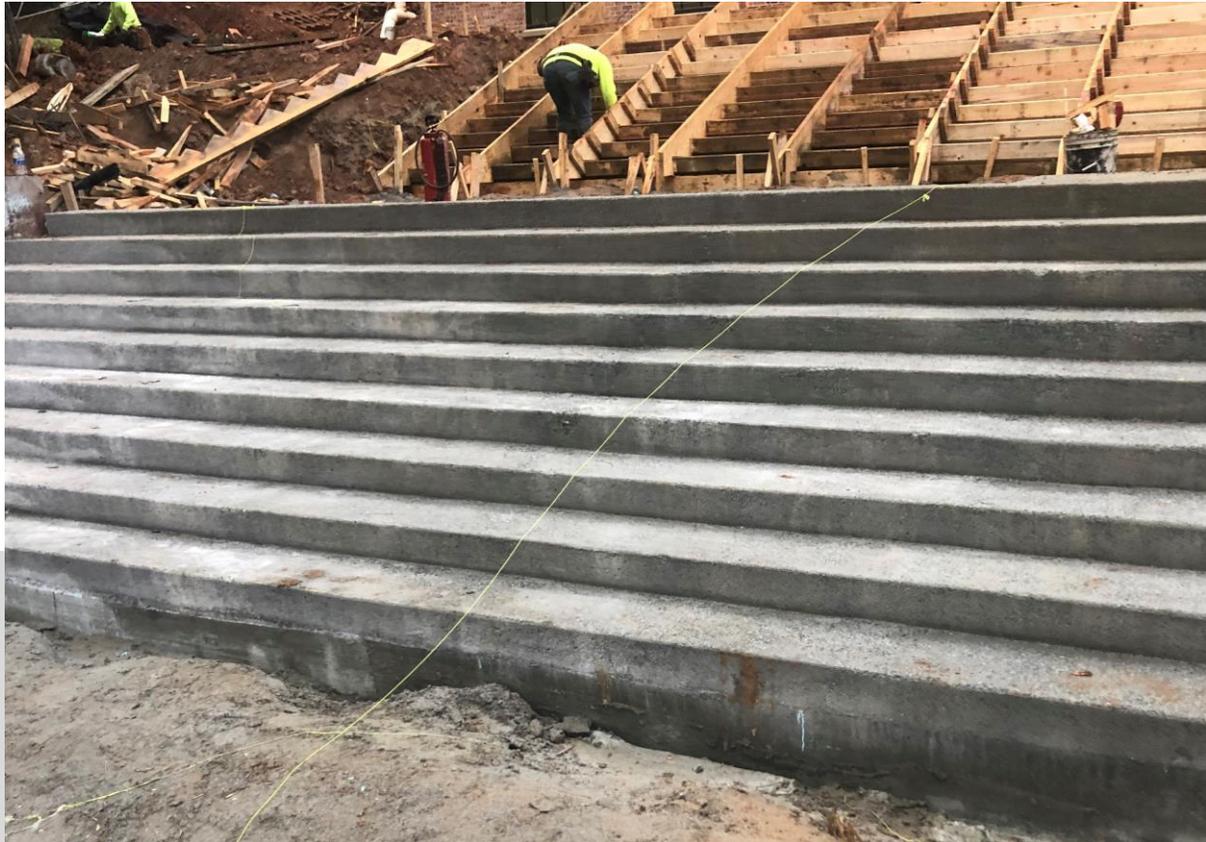

Hardscape Progress South East Elevation



Photo Updates

North Elevation Grading Progress



ACT Ceiling Progress 3rd Floor



Photo Updates

Gypsum Board Progress at Lower Media Center Ceilings



Gypsum Board Progress in Media Center Double Height Space

