

WEEKLY CONSTRUCTION PROGRESS REPORT


Atlanta College and Career Academy

November 01, 2019



Prepared For: Atlanta Public Schools

Prepared By: Tony Washington

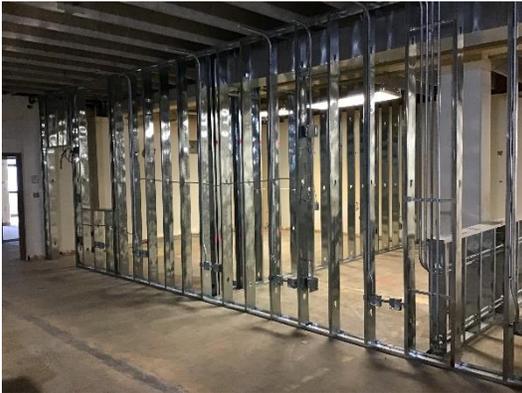

Electrical Rough-In at Second Floor



Underground Plumbing at Nursing & Dental Labs



Underground Plumbing at Hallway



CMU Block Infill at Culinary Arts Lab



Structural Supports for Roof Openings



Second Floor Classroom Framing

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

November 01, 2019



Last Week's Activities:

- Began saw cutting for underground plumbing
- Began second floor ductwork installation
- Began interior framing
- Continued second floor interior framing
- Continued selective interior demolition
- Continued selective MEP demolition

This Week's Activities:

- Began CMU block infill
- Began structural supports for concrete deck openings
- Completed saw cutting for underground plumbing
- Began underground plumbing
- Continued second floor ductwork installation
- Completed selective interior demolition
- Completed selective MEP demolition
- Continued interior framing

Next Week's Activities:

- Continue structural supports for concrete deck openings
- Continue second floor ductwork installation
- Continue underground plumbing
- Begin saw cutting at Automotive & Aviation Lab
- Continue interior framing
- Complete CMU block infill

Schedule:

- Status: On Schedule

Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,043,624
