

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

February 20, 2020



**Prepared For:** Atlanta Public Schools

**Prepared By:** Tony Washington




Kitchen Hood Installation at Culinary Arts Lab




Walk-In Cooler/Freezer Installation




Drywall Prep for Paint at Graphics Lab

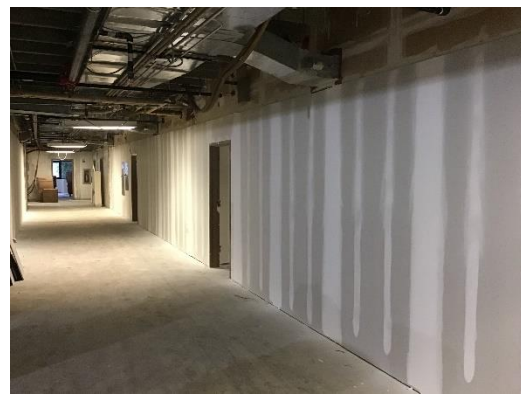

Drywall Prep for Paint at 2<sup>nd</sup> Floor Corridor

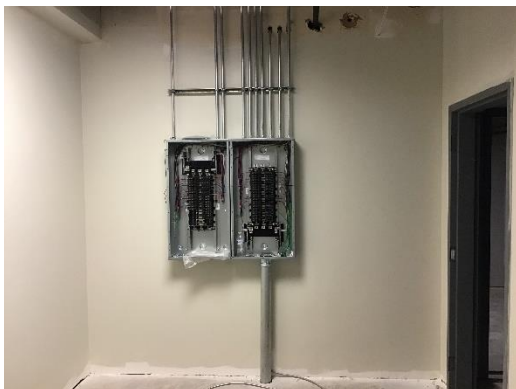

Electrical Panelboard Installed

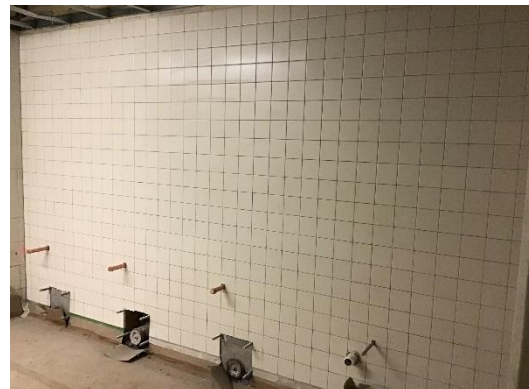

Wall Tile Installation at 2<sup>nd</sup> Floor Restroom

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

February 20, 2020



### Last Week's Activities:

- Continued sprinkler piping at the first floor
- Continued CMU block installation for openings at Auto/Aviation Labs
- Continued electrical panel installation
- Began second floor wall prep. for paint
- Continued first floor drywall installation
- Continued installation of hollow metal frames at the main building
- Continued installation of rooftop condensers
- Continued installation of kitchen hoods at Cafeteria Kitchen
- Continued installation of kitchen hood exhaust fans
- Began priming walls at Auto/Aviation Labs
- Began second floor controls wiring at second floor
- Continued second floor ceiling grid installation

### This Week's Activities:

- Continued sprinkler piping at the first floor
- Completed CMU block installation for openings at Auto/Aviation Labs
- Continued electrical panel installation
- Continued drywall installation at main building
- Continued second floor wall prep. for paint
- Continued painting walls at second floor
- Began wall tile installation at restrooms
- Continued installation of hollow metal frames at the main building
- Continued installation of kitchen hoods at Cafeteria Kitchen
- Began installation of the walk-in cool/freezer
- Continued priming walls at Auto/Aviation Labs
- Continued HVAC controls wiring at the second floor
- Backfilled sanitary grease traps

### Next Week's Activities:

- Continue sprinkler piping at the first floor
- Begin demolition of CMU block at Auto/Aviation Lab Openings
- Continue wall tile installation at restrooms
- Begin new water line installation
- Continue electrical panel installation
- Continue second floor wall prep. for paint
- Complete first floor drywall installation
- Continue second floor ceiling grid installation
- Complete installation of kitchen hoods at Culinary Arts Lab
- Continue second floor ceiling grid installation

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

February 20, 2020



### Schedule:

- Status: On Schedule

### Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$4,190,919
