

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

June 19th, 2020



**Prepared For:** Atlanta Public Schools

**Prepared By:** Tommy Pease




Installation of Kitchen Equipment in the Culinary Arts Lab 136



Installation of Auto Equipment in the Automotive Lab 166



Installation of Markerboards in Fire & Emergency Services 233

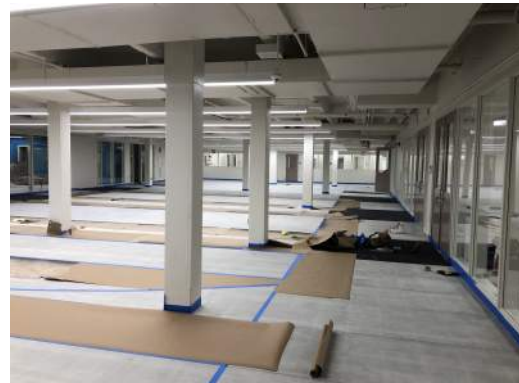

Installation of the Sealed Concrete Floor in the First Floor Commons 156



Installation of Dental Equipment in the Dental Lab 123



Installation of Casework and Countertops in the Nursing Lab 129

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

June 19th, 2020



### Last Week's Activities:

- Continued sealed concrete flooring installation at first floor
- Continued sprinkler headdrop at first floor
- Continued installation of wood doors
- Continued installation of casework and countertops
- Continued kitchen equipment connections in the Culinary Arts Lab
- Continued installation of Ansul systems in kitchen hoods
- Continued installation of HVAC controls.
- Continued installation of electrical devices
- Continued testing fire alarm system
- Completed paving and striping
- Completed installation of sealed concrete floor in the Aviation Lab
- Began final cleaning
- Began installation of lockers

### This Week's Activities:

- Continued sealed concrete flooring installation at first floor
- Continued installation of doors and door hardware
- Continued final coat of paint on first floor
- Continued installation of Ansul systems in kitchen hoods
- Continued installation of lockers
- Continued final cleaning
- Continued kitchen equipment connections
- Continued HVAC startup
- Completed installation of casework and countertops
- Completed installation of carpet and base on the second floor
- Completed installation of HVAC controls.
- Completed installation of electrical devices
- Completed sprinkler head drop at first floor

### Next Week's Activities:

- Continue kitchen equipment connections
- Complete installation of lockers
- Complete installation of doors and door hardware
- Complete sealed concrete flooring installation at first floor
- Complete final coat of paint on the first floor
- Complete installation of Ansul systems in kitchen hoods
- Complete HVAC start up

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

June 19th, 2020



### Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$8,971,147
