

Ongoing Activities

01/21/19 – 01/25/19

- Erecting sequence 4 & 5 steel
- Poured 2nd level west elevated slab
- Framing lower level parapet and exterior walls
- Installing lower level interior/exterior block walls
- Installing main level overhead MEP
- Installing lower level roof

Upcoming Activities

- 3rd level west elevated slab pour
- Continue erecting sequence 4 & 5 steel
- Complete lower level block walls
- Continue installing lower level roofing
- Continue framing exterior walls on main level
- Topping out celebration

Financial & Schedule Status

Current GMP = \$27.6M
Bill to Date = \$7,897,109


Start Date: July 2, 2018
Current Completion Date:
July 10, 2019

Project Overview



Photo of the project site from overhead looking south

Safety Sector

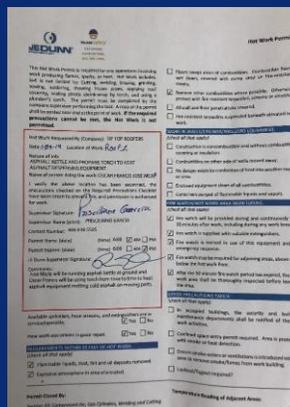

“Hot Work Permit”

A hot work permit is required for any operations involving work producing flames, sparks, or heat. Hot Work includes, but is not limited to: Cutting, welding, brazing, grinding, sawing, soldering, thawing frozen pipes, applying roof covering, sealing plastic shrink-wrap by torch, and using a plumber’s torch.



Exterior brick installed on lower level south wall



2nd level west elevated slab pour in progress



Main and 2nd level provided with temp heat and enclosure to facilitate 2nd level concrete pour



Corridor C3-2 on main level east looking west
