

Ongoing Activities

11/12/18 – 11/16/18

- Below grade waterproofing on retaining wall
- Lower level underground electrical rough-in
- Install lower level vapor barrier for SOG
- Layout and installation of rebar for main level footings
- Removing standing water from jobsite following heavy rains

Upcoming Activities

- Lower level slab on grade pour
- Continue waterproofing walls at lower level
- Continue backfilling at lower level retaining wall
- Continue main level foundations
- Commence main level underground MEP

Financial & Schedule Status

Current GMP = \$27.6M
Bill to Date = \$3,690,041

Start Date: July 2, 2018
Current Completion Date:
July 10, 2019

Project Overview



Photo of the project site from main level looking South

Safety Sector



“Trenching Spoils”

OSHA requires spoils from trenching activities be piled a minimum of 2' away (4' is preferred) from the edge of the trenching location. This is to minimize the chance of spoils re-entering the location while workers are present.




Lower level prep for SOG



Lower level vapor being barrier installed for SOG pour



Insect treatment applied to base ahead of SOG

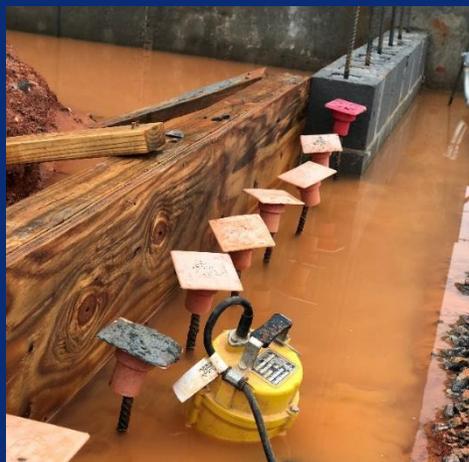

Removing all standing water following heavy rains
