



Brown & Root
INDUSTRIAL SERVICES, LLC.

DAILY CONSTRUCTION PROGRESS REPORT

Construct Field Houses, S. Atlanta and Carver High Schools

March 10, 2021

Prepared For: Atlanta Public Schools

Prepared By: Michael Bower



Figure 1 S. Atl –CMU to extend to deck

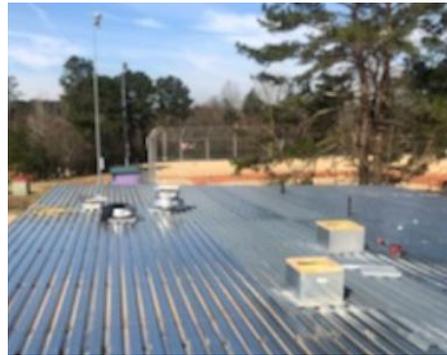


Figure 2 S. Atl – Mechanical Roof Curbs



Figure 3 Carver –Steel Erector Mobilization, Steel Decking



Figure 4 Carver – Roof Steel



Brown & Root
INDUSTRIAL SERVICES, LLC.

DAILY CONSTRUCTION PROGRESS REPORT

Construct Field Houses, S. Atlanta and Carver High Schools

March 10, 2021



Figure 5 – Carver Steel Deliveries

Today's Activities:

- Carver HS –Additional steel deliveries, on-site fabrication of roof steel sections at ground level, erection pending arrival of boom truck this afternoon.
- S. Atlanta HS – Mechanical roof curbs delivery and installation, cmu walls top out to deck in between steel beams, glass block delivery.
