


Quote of the week: "Don't let yesterday take up too much of today."

Project: FL Stanton ES Renovation and addition

Week Ending: September 22, 2023

- Re-roof of Building 1998, Art Building completed
- Erosion Control of north side of site started
- Temporary lighting installed

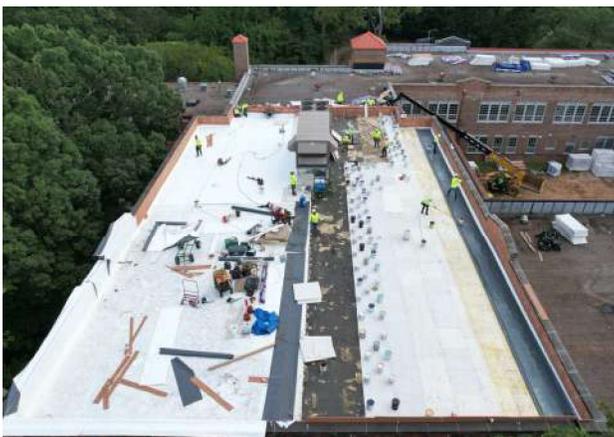

NEXT WEEK – September 25 - September 29

- Complete Erosion Control
- Complete 7 walk walk
- Complete Roofing of 1928
- Start Clearing
- Installing BMPs

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Kha Huynh, Carroll Daniel Construction Co.
