


Quote of the week: "Don't let yesterday take up too much of today."

Project: FL Stanton ES Renovation and addition

Week Ending: September 15, 2023

- Light fixture layout is complete
- Contour came out to begin drilling at the stairwell in the new media center
- Installed silk fence for erosion control
- Rock Removal on the Roof is complete

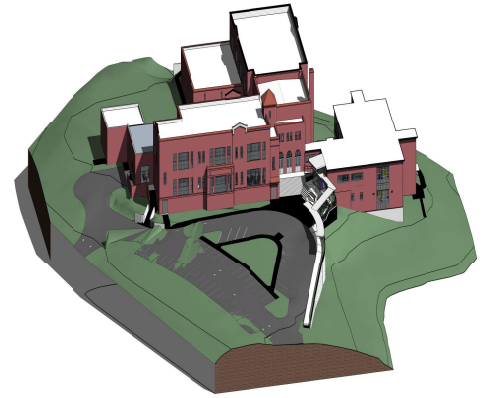

Rock removal on the roof is complete



Begin Drilling in the stairwell area in the old auditorium

NEXT WEEK – September 18 - September 22

- Begin saw-cutting trenches for underground plumbing
- Begin roofing replacement at wet areas.
- Resume MEP rough- in
- Continue erosion BMPs
- Resume installing new duct throughout

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
