

**Joke of the Week:** What kind of bird works on a construction site? A Crane

## Project: Hank Aaron Academy Additions & Modifications

**Week Ending: August 8, 2025**

### THIS WEEK:

- Blockfill continues classroom areas
- Dryfall painting completed in gymnasium
- Painting started in stage area
- Ceiling grid framing ongoing
- Sheetrock ceiling installation continues
- Wire terminations at boxes in progress
- Lighting installed in low roof area grid
- Canopies installed



*Exterior view - ramp entrance*



*Exterior view – delivery entrance*




*Light installation ongoing*



*Stage area dryfall started*



*Ceiling grid installation ongoing*

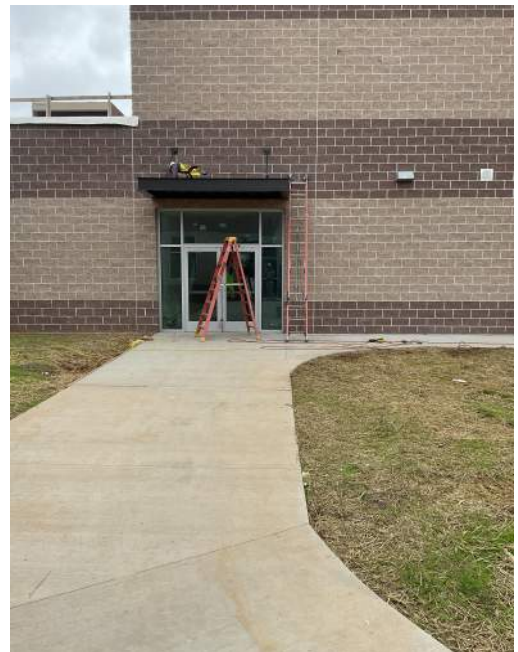

*Canopy install*





*Locker room sheetrock ceiling complete*



*East side exterior view*

NEXT WEEK – Aug 11 - Aug 15

- Complete fire sprinkler overhead rough-in stage area
- Continue overhead rough-in such as pulling wires, installing lighting
- Continue sheetrock ceiling installation
- Continue painting in stage area
- Install interior doors
- Install epoxy flooring

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- December 31, 2025

PREPARED BY:

Karee Shaw, Carroll Daniel Construction Co.

