



Weekly Construction Progress Report

Grady High School

Week Ending: 4/24/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Parrish has continued to take measures to comply with the CDC and OSHA recommendations to keep the jobsite safe
- Continue to finish Building Pad on East side of New Addition, including relocation of Underground Utilities
- Removal of acoustical ceiling tile and grid in the Theater Building
- Removal of duct work to make room for new duct work in 8th Street Building
- Plumbing Fixtures removed from 8th Street Building for new Fixtures
- Install new plumbing piping for new lavatories
- Installation of new storm piping
- Installed 134 Geopiers on the West side of the New Addition, will come back on Tuesday to finish
- Removal of Theater Seats

NEXT WEEK – 4.27.2020 – 5.01.2020

- Completion of Geopier System
- Begin Digging Foundations Monday 4/27
- Begin Stormwater Detention System Installation
- Reface CMU Block in Gang bathrooms for new Ceramic Tile
- MEP rough-in above ceiling in all corridors
- Grady High School teachers to start removing personal items to prepare for classroom work for Summer 2020 work.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 970,824.26

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - John Rood, PCG
 - Barry Tucker, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG



Photo Updates

Installation of New Storm Piping on East Side of the New Addition



Storm Drain Completed on East Side of the New Addition



Photo Updates

Installation of Geopier System




Installation of Geopier System



Photo Updates

Plumbing Fixtures Removed from 8th Street Building

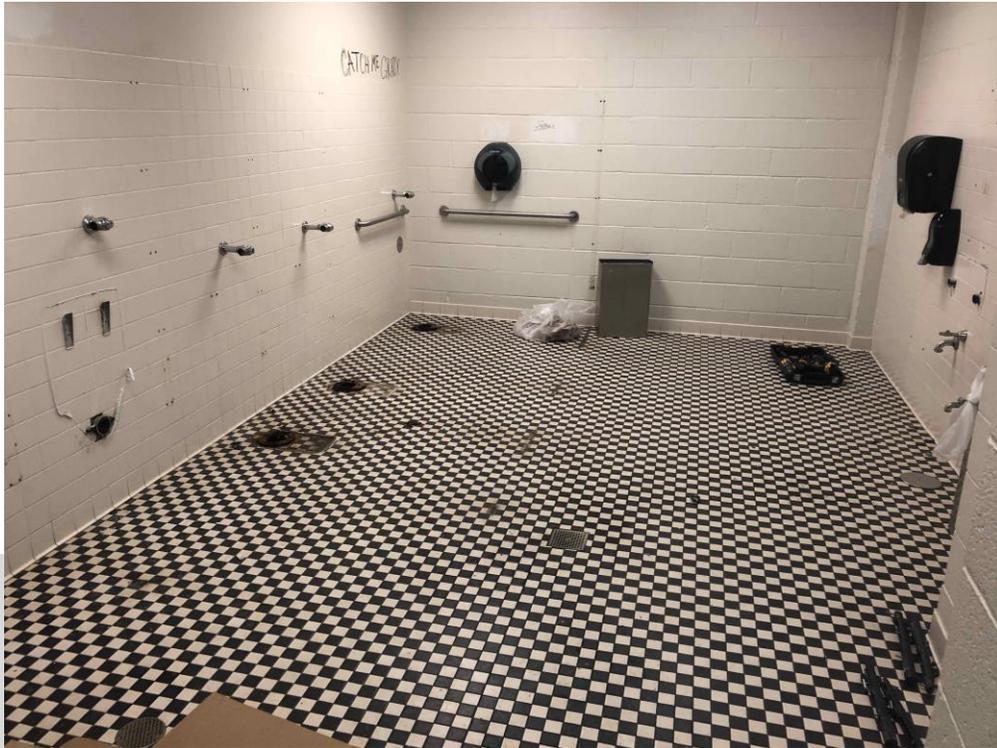


New Plumbing Piping installed for new Lavatories in 8th Street Building



Photo Updates

Removal of Ceiling Tiles and Ceiling Grid in Theater Building

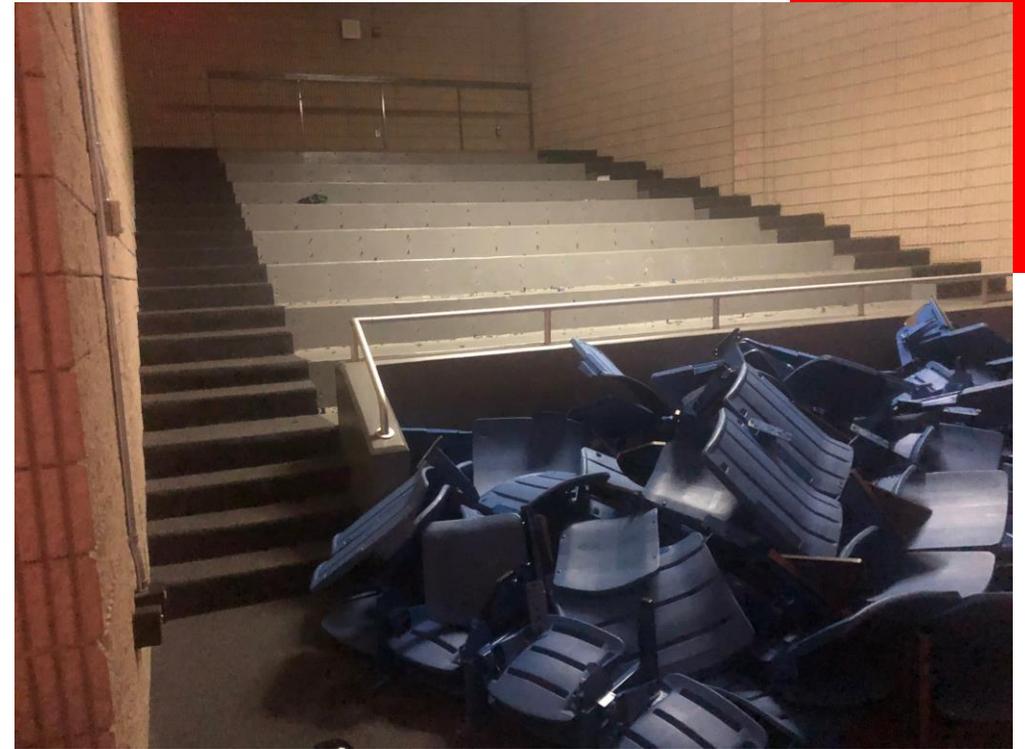

Removal of old Seating in the Theater Building

