



Weekly Construction Progress Report

Grady High School

Week Ending: 5/29/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Parrish has continued to take measures to comply with the CDC and OSHA recommendations to keep the jobsite safe
- Poured remainder of South Wall at new addition building
- MEP rough-in above ceiling and on Roof
- Continue Remove ACT Ceilings in classrooms
- Continue tear off and replacement of Theater Building Roof
- Continuing TPO Install on 8th Street Building
- Installation of Water Source Heat Pumps
- Installation of steel reinforcements
- Painting in Theater Building
- Ceramic Tile Installation in 8th Street Group Bathrooms
- Jack and Bore into manhole on 10th Street
- Masonry Restoration

NEXT WEEK – 6.01.2020 – 6.05.2020

- MEP rough-in above ceiling and on Roof
- Continue installing Water Source Heat Pumps
- Continue TPO Roof install at 8th street and Theater buildings
- Begin Epoxy in 8th Street Single Bathrooms
- Continue Masonry Restoration
- Demo ACT ceilings in classrooms in 8th Street
- Install storm and sewer lines for new addition
- Waterproofing wall and installing foundation drainage system
- Painting in Theater and 8th Street Building
- Begin Basement Steel Decking
- Begin Grading Parking Lot
- Begin ACT Ceilings in theater



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 3,808,514.49

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule




ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG



Photo Updates

Wall forms removed on South Wall of New Addition

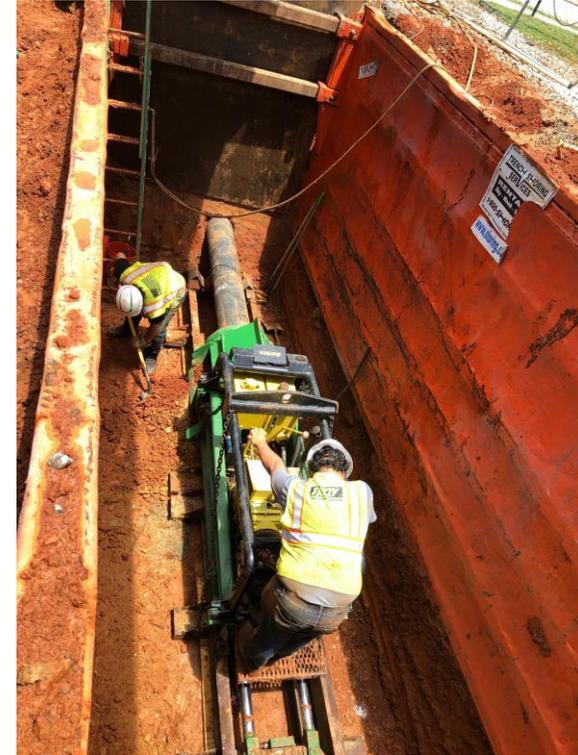


Jack and Bore to 10th Street Manhole for Sanitary Sewer at New Addition



Photo Updates

Installation of Water Source Heat Pumps in 8th Street Building Corridors

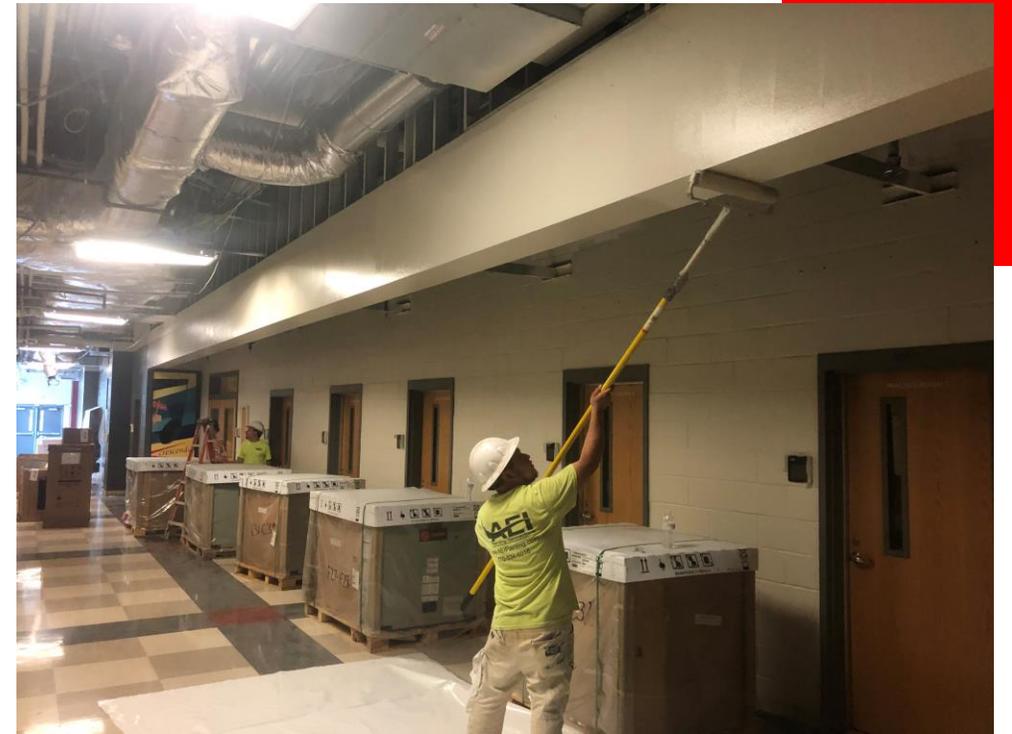

Painting in Theater Building



Photo Updates

New Epoxy completed in 8th Street Group
Bathrooms




Infill existing openings for new family living
center restroom



Photo Updates

Installing Joist Reinforcement for new Energy Recovery Units to be installed on the roof

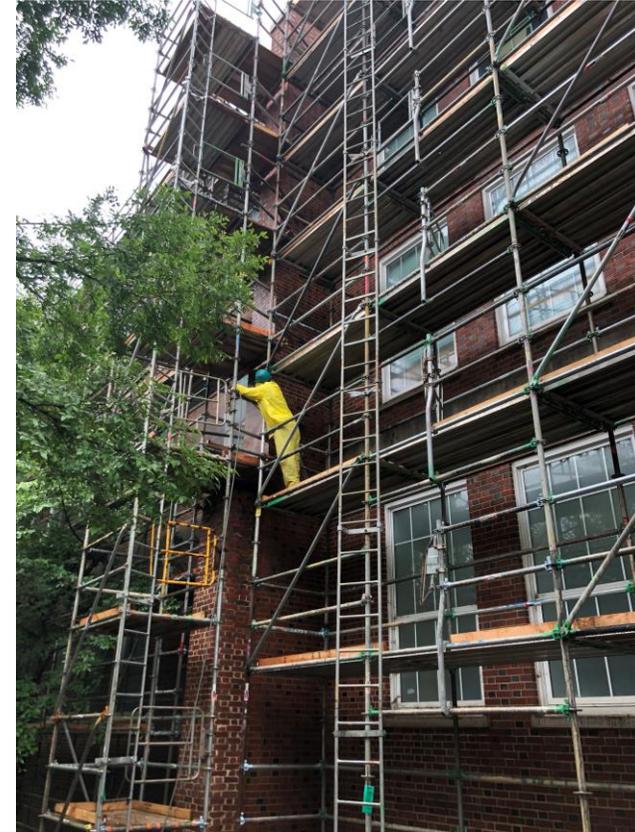

Cleaning for Masonry Restoration at Charles Allen Building

