



Frederick Douglass High School Fieldhouse

Client: Atlanta Public Schools

Architect: JW Robinson & Associates

Contractor: CD Moody Construction Company




FD- Food Equipment Installation



FD- Exterior



FD- Pump Station Controls

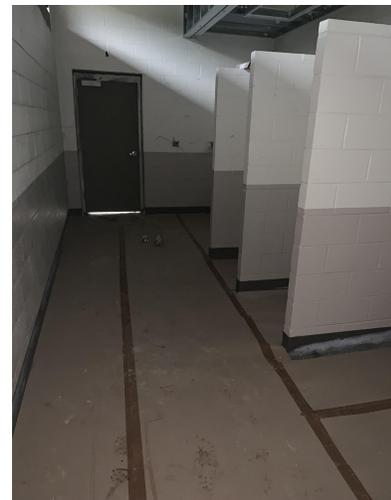

FD- Epoxy Flooring Finish and Cover

Frederick Douglass Fieldhouse

Current Activity: Glass Block Install, Drywall

Upcoming Activity: Toilet Partitions, Accessories, Permanent Power

Contract Value: \$621,805

Billed to Date: \$436,650

Substantial Completion Date: November 25th, 2019
